



ISTANBUL RESILIENCE PROJECT

**PROFİLO VOCATIONAL AND TECHNICAL
ANATOLIAN HIGH SCHOOL**

**ENVIRONMENTAL AND SOCIAL MANAGEMENT
PLAN**

JULY 2026

ISTANBUL RESILIENCE PROJECT

Contents

List of Annexes	3
List of Tables.....	3
List of Figures	3
Abbreviations	4
1. Executive Summary	6
2. Introduction	8
3. Legal and Institutional Framework	9
4. General Project and Project Area Information	10
4.1 Project Description.....	10
4.2 General Information and Objectives	10
4.3 Subproject Description and Activities.....	12
5. Environmental and Social Management Plan.....	14
6. Roles and Responsibilities.....	31
7. Capacity Building and Training	33
8. Implementation Schedule and Cost Estimates.....	34
9. Stakeholder Engagement and Grievance Mechanism	35
10. Contractor’s Reference Documents.....	38
11. Review and Approval.....	38
ANNEXES	39

ISTANBUL RESILIENCE PROJECT

List of Annexes

Annex 1. Site Photographs	40
Annex 2. Aerial View of the Project Site and Surroundings.....	43
Annex 3. Land Registration Documents	45
Annex 4. Topographic Survey.....	46
Annex 5. Zoning Status Letter	47
Annex 6. Official Invitation Letter for the Public Information and Consultation Meeting.....	48
Annex 7. Public Announcement of the Consultation Meeting.....	49
Annex 8. Minutes of the Public Information and Consultation Meeting	50
Annex 9. Site-Specific ESMP Presentation Materials.....	53
Annex 10. Project Design Presentation	59
Annex 11. Consultation Meeting Photographs.....	63

List of Tables

Table 1 Environmental and Social Management Plan.....	15
Table 2 Roles and Responsibilities.....	31
Table 3 Indicative ESMP Implementation Budget.....	34

List of Figures

Figure 1: General View of Profilo Vocational and Technical Anatolian High School (Kağıthane, Istanbul).....	12
---	----

ISTANBUL RESILIENCE PROJECT

Abbreviations

AoI	Area of Influence
CERC	Contingent Emergency Response Component
CHS	Community Health and Safety
CİMER	Presidency's Communication Center
CoC	Code of Conduct
C-ESMP	Contractor Environmental and Social Management Plan
EIA	Environmental Impact Assessment
ERP	Emergency Response Plan
ESF	Environmental and Social Framework
ESHS	Environment, Social and Health and Safety
ESMF	Environmental and Social Management Framework
ESMP	Environmental and Social Management Plan
ESSs	Environmental and Social Standards
E&S	Environmental and Social
GBV	Gender-based Violence
GM	Grievance Mechanism
IMM	Istanbul Metropolitan Municipality
IPCU	Istanbul Project Coordination Unit
IRP	Istanbul Resilience Project
LMP	Labor Management Procedures
LM Plan	Labor Management Plan
MoNE	Ministry of National Education
MSDS	Material Safety Data Sheet
OHS	Occupational Health and Safety
PPE	Personal Protection Equipment
SEA/SH	Sexual Exploitation and Abuse/Sexual Harassment
SEP	Stakeholder Engagement Plan
WB	World Bank
WHO	World Health Organization

ISTANBUL RESILIENCE PROJECT

WWTP Wastewater Treatment Plant
YİMER Foreigners Communication Center

ISTANBUL RESILIENCE PROJECT

1. Executive Summary

The Istanbul Resilience Project (IRP), financed by the World Bank and implemented by the Istanbul Project Coordination Unit (IPCU), aims to enhance disaster and climate resilience in Istanbul Province by strengthening emergency preparedness, reducing disaster risks, and ensuring that critical public facilities remain fully functional during and after disasters.

The Project is structured under four components:

1. Strengthening the Emergency Preparedness and Response System
2. Enhancing the Resilience of Critical Public Buildings and Facilities
3. Project Management and Technical Assistance
4. Contingent Emergency Response Component (CERC).

Within the scope of Component 2, the reconstruction of *Profilo Vocational and Technical Anatolian High School in Kağıthane, Istanbul*, has been selected as one of the subprojects to be financed under the IRP. The school building, previously assessed as structurally vulnerable, has been demolished and will be reconstructed in line with the highest seismic and climate resilience standards. Reconstruction at the original location is not feasible due to urban planning constraints related to transportation corridors and planned municipal infrastructure projects. The school will therefore be reconstructed on an alternative site owned by Kağıthane Municipality and designated for educational use, while the former site is intended to be transferred to the municipality for public use. The relocation of the school has been completed through an inter-institutional arrangement between public entities. The new facility will serve not only as an educational institution but also as a self-sufficient post-disaster shelter, ensuring continuity of critical services in the aftermath of emergencies.

Key features of the subproject include:

- **Nearly Net-Zero Quality Building:** Designed with energy-efficient systems (aligned with Turkish TS825 and IRP's Class B performance standards), renewable energy installations (such as photovoltaic panels), and enhanced generator capacity.
- **Water Security and Storage:** Equipped with additional storage tanks and rainwater harvesting systems to ensure uninterrupted water supply during disasters.
- **Emergency Preparedness:** Integration of communication systems and basic provisions (electricity, water, and food) for at least the first 72 hours after a disaster, supporting both students and surrounding communities.
- **Inclusive Design/Universal Access:** The facility will include tactile surfaces, ramps, elevators, and accessible sanitary facilities, ensuring universal access, particularly for persons with disabilities and other vulnerable groups.
- **Community Shelter Function:** The school has been designed with potential to host displaced individuals during emergencies, contributing to the post-disaster shelter capacity of Istanbul.

The environmental and social screening confirmed that the project does not fall under ineligible activities of the IRP Exclusion List and is categorized as *Moderate Risk* under the World Bank's Environmental and Social Framework (ESF). The main anticipated risks include:

- **Construction-related risks:** dust, noise, traffic disruptions, and construction waste generation.
- **Occupational Health and Safety (OHS) risks:** hazards from heavy equipment, work at height, handling of materials, and potential risks of electrical accidents during construction activities.
- **Community Health and Safety risks:** possible exposure to dust/noise and minor increases in local traffic.
- **Waste Management:** construction debris and other solid and liquid wastes will require careful monitoring, segregation, and management to ensure recycling and safe disposal in line with national regulations and the IRP Environmental and Social Management Framework (ESMF).

ISTANBUL RESILIENCE PROJECT

Mitigation measures have been developed and will be implemented in line with the IRP's Environmental and Social Management Framework (ESMF), Labor Management Procedures (LMP), and Stakeholder Engagement Plan (SEP). This site-specific Environmental and Social Management Plan (ESMP) will be applied to ensure compliance with Turkish regulations and the World Bank's Environmental and Social Standards (ESSs).

A dedicated Grievance Mechanism (GM) will be available for all project stakeholders, including workers and community members, to raise concerns, complaints, or suggestions related to the subproject. The GM will be accessible, transparent, and inclusive, ensuring timely responses and effective resolution. Special channels will be provided for sensitive cases, including issues related to Sexual Exploitation and Abuse/Sexual Harassment (SEA/SH), with confidentiality and survivor-centered procedures guaranteed.

The reconstruction of Profilo Vocational and Technical Anatolian High School will thus contribute directly to IRP's objectives by providing a safe, resilient, green, and inclusive public facility that enhances educational continuity, protects vulnerable groups, and supports emergency response capacity in Kağıthane and beyond.

ISTANBUL RESILIENCE PROJECT

2. Introduction

This ESMP has been prepared for the reconstruction of Profilo Vocational and Technical Anatolian High School under the IRP, financed by the World Bank and implemented by the IPCU.

The purpose of this ESMP is to identify the potential environmental and social risks and impacts of the subproject and to propose appropriate mitigation and monitoring measures. The ESMP ensures that project activities are implemented in compliance with the World Bank ESF, particularly the relevant ESSs, as well as with applicable Turkish laws and regulations, including the Law on Environment No. 2872 (1983) and national labor, occupational health and safety legislation.

The mitigation measures defined in this ESMP will be included in the bidding documents, and their implementation will be ensured by the Contractor under the supervision of IPCU and the Supervision Consultant. This ESMP is a living document and will be updated as necessary during implementation to reflect site conditions, monitoring results, and stakeholder feedback.

ISTANBUL RESILIENCE PROJECT

3. Legal and Institutional Framework

This ESMP has been developed in line with the World Bank Environmental and Social Framework (ESF) and the relevant Environmental and Social Standards (ESSs), as well as with Turkish national laws and regulations governing environment, labor, occupational health and safety, and construction.

Key applicable legislation includes the Environment Law No. 2872, the Labor Law No. 4857, the Occupational Health and Safety Law No. 6331, and related secondary regulations. In cases where discrepancies arise between national legislation and the WB's ESF, the requirement that ensures a higher level of environmental and social protection will apply.

The implementation of this ESMP will be ensured through the institutional arrangements of the IPCU, with monitoring and supervision carried out by the supervision consultant, and day-to-day compliance ensured by the contractor.

The IRP ESMF is publicly disclosed and can be accessed at the following links:

[Turkish Version](#)

[English Version](#)

ISTANBUL RESILIENCE PROJECT

4. General Project and Project Area Information

Türkiye faces significant disaster risks due to its seismicity, urbanization, and growing population. The IRP has been designed to address these risks by strengthening critical public buildings and ensuring that they can remain operational during and after disasters. Within this framework, the reconstruction of Profilo Vocational and Technical Anatolian High School has been selected as one of the subprojects to be financed under *Component 2: Enhancing the Resilience of Critical Buildings and Facilities*.

The main objective of the subproject is to rebuild the school to the highest seismic and climate resilience standards, while equipping it as a self-sufficient post-disaster shelter capable of providing basic services (electricity, water, food, and communication) during the first 72 hours of a disaster. The project will therefore contribute to strengthening preparedness, supporting emergency response capacity, and ensuring continuity of education.

Construction activities will consist of new building works (excavation, reinforced concrete, finishing works, and landscaping) on the site where the former structurally weak building has already been demolished and cleared. These activities are expected to generate temporary, localized, and manageable environmental and social impacts, such as noise, dust, traffic, and waste.

Based on the current scope and applicable Turkish EIA Regulation, the subproject is not subject to a full EIA process; however, all applicable environmental, occupational health and safety, and construction management requirements will be complied with.

This ESMP has therefore been prepared as a guidance document to identify potential risks, propose mitigation measures, and ensure that construction and operation activities are carried out in line with both national regulations and the World Bank ESF.

4.1 Project Description

Subproject Title:	Reconstruction of Schools (Nearly Net-Zero Quality, Self-Sufficient Post-Disaster Facility)
Location:	Merkez District, Begonvil Street, Kağıthane / Istanbul 7035 Block / 3 Plot
Implementing Institution:	Istanbul Project Coordination Unit (IPCU)
Responsible User Institution:	Ministry of National Education (MoNE)
Site Condition:	The newly designated project site is currently vacant and ready for the commencement of construction works. Education activities are temporarily continued in another facility, as coordinated and arranged by the Ministry of National Education (MoNE) in line with its official procedures.
Building Information:	Planned as one block-building, with an approximate enclosed area of 14,335.02 m ² .
Estimated Cost:	The project consists of 14,335.02 m ² of enclosed area, and relevant authorities should develop their own cost estimations as appropriate.
Construction Period:	18 months (Approx.)

4.2 General Information and Objectives

Kağıthane is a district located on the European side of Istanbul, within the Marmara Region of Türkiye. The district is characterized by a dense urban environment comprising residential neighborhoods,

ISTANBUL RESILIENCE PROJECT

commercial areas, public institutions, and rapidly developing business centers. Historically associated with industrial activities along the Kağıthane Stream, the district has undergone significant urban transformation and redevelopment over recent decades. Strategically positioned near major transportation corridors and central business districts, Kağıthane benefits from extensive public transportation networks, including metro connections and major road infrastructure. Ongoing urban regeneration projects, new residential developments, and expanding commercial investments have contributed to the district's evolution into a dynamic mixed-use urban center that combines residential, commercial, educational, and service functions. The subproject site is situated in Merkez District of Kağıthane, at Begonvil Street, Parcel 7035/3. The project site is state-owned land under the Kağıthane Municipality and has been allocated to the Ministry of National Education. According to the applicable zoning plans, the designated land use function is "Vocational and Technical Education Facility Area."

The newly designated site is currently vacant; furthermore, the former structurally weak school building has been demolished at the original school location. Education activities for Profilo Vocational and Technical Anatolian High School are temporarily being carried out in another educational building to avoid disruption during construction, in coordination with the Ministry of National Education (MoNE) and in line with its established procedures.

Building Location

The subproject area is easily accessible by local roads and is connected to Kağıthane district center by public and private transport options.

The Area of Influence (AoI) is defined at the neighborhood scale, covering the broader built-up area in which the project site is located, including surrounding residential areas and nearby public facilities. These receptors may be affected by temporary construction-related impacts such as noise, dust, and traffic. Based on the surrounding receptors identified within the AoI, the main sensitive receptors are as follows (approx. straight-line distances):

- **Residential and commercial buildings:** The project site is located within a densely developed urban area characterized by residential and commercial buildings. Several commercial establishments, including hotels, shopping center, gross markets, are located within the project site AoI.
- **Educational facilities:** Several educational facilities are located within the AoI. These include Kağıthane Anatolian Highschool (~250 m), İstanbul Kent University Kağıthane Campus (~165 m), and Sadabad Highschool Male Student Dormitory (~258 m) from the project site center.
- **Healthcare facilities:** Healthcare services are available within the AoI. Yeni Huzur Medical Center is located approximately ~260 m from the project site center.
- **Religious facilities:** Religious facilities are present within the AoI. T.C. Kağıthane Müftülüğü Ayazma Mosque is located approximately ~230 m from the project site center.
- **Government/public facilities:** Public and social facilities within the AoI include İSKİ Kağıthane Branch Directorate (~175 m), Zafer Park (~315 m), Kağıthane Municipality Cleaning Services Directorate (~380 m), Sadabad Police Station (~560 m), Ayazma Park (~300 m), Axis Shopping Mall (~250 m), and Delta Hotels İstanbul Kağıthane (~165 m).
- **Infrastructure:** No major infrastructure facilities (such as water reservoirs, treatment plants, or energy facilities) have been identified in close proximity to the project site.
- **Transportation infrastructure:** No metro or railway lines are located in close proximity to the project site.

Community Health and Safety (CHS) risks will be managed through the ESMP and Contractor ESMP (C-ESMP), including relevant sub-plans such as the Traffic Management Plan. Particular attention will be given to sensitive receptors within the AoI, especially nearby educational facilities, and communication will be maintained during construction to minimize disturbances.

A general view of the project site is presented in Figure 1.

ISTANBUL RESILIENCE PROJECT

Site photographs (Annex 1) — including views of the project area from different perspectives — as well as satellite and aerial imagery (Annex 2) and land registry records (Annex 3) are provided in the annexes to this ESMP. In addition, a location map showing the project site and nearby infrastructure is presented in Annex 2.

Annex 3 (Land Register) presents the official title deed information for the project site, including the parcel and block numbers, total land area (14,335.02 m²), land use designation (Vocational and Technical Education Facility Area), and registration under the Kağıthane Municipality, confirming public ownership. The allocation to the Ministry of National Education for educational purposes has been formalized through official correspondence issued by the Istanbul Governorship and relevant institutions. Annex 4 (Topographic Survey) provides detailed information on the site's existing elevation, boundaries, and physical features, supporting the design and layout of the new school building. Annex 5 (Zoning Status Letter) includes the official confirmation of the land-use designation and verifies that the site is planned as a Vocational and Technical Education Facility Area under the applicable zoning plans.

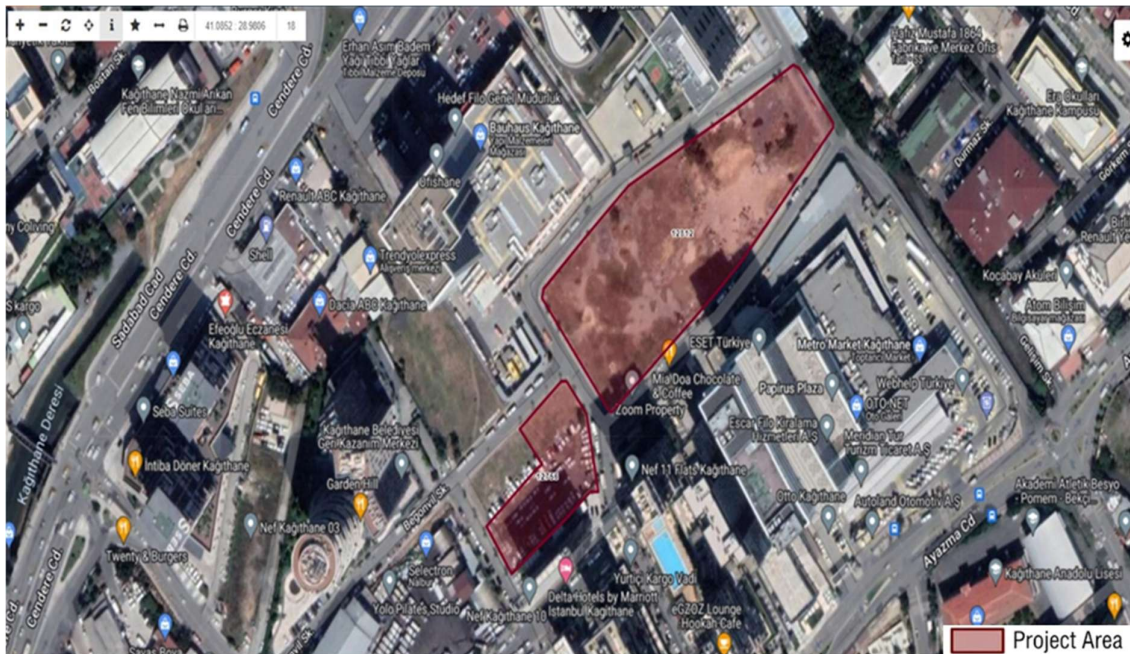


Figure 1: General View of Profilo Vocational and Technical Anatolian High School (Kağıthane, Istanbul)

4.3 Subproject Description and Activities

The subproject consists of the reconstruction of Profilo Vocational and Technical Anatolian High School in Kağıthane, Istanbul. The former school building, identified as structurally weak, has already been demolished. The newly designated project site is currently vacant and ready for construction works.

The new school will be constructed as a single-block building with a total enclosed area of approximately 14,335.02 m². It will be designed to meet the highest seismic and climate resilience standards and to function as a self-sufficient post-disaster shelter. Key design features include:

- Additional water storage capacity,
- Renewable energy systems (such as photovoltaic panels),
- Expanded generator capacity, and
- Enhanced communication systems to ensure building functionality during emergencies.

ISTANBUL RESILIENCE PROJECT

Planned construction activities include:

- Site preparation and excavation,
- Reinforced concrete and superstructure works,
- Interior and exterior finishing works,
- Landscaping and external arrangements, and
- Procurement and installation of building materials and equipment.

No major new infrastructure such as transportation routes, electricity, water, or wastewater lines is required, as the site is already serviced by existing urban infrastructure.

Construction activities are expected to generate typical short-term environmental and social impacts such as dust and noise emission, generation of construction waste, increased traffic, and potential risks to community health and safety (CHS) and occupational health and safety (OHS). These impacts will be mitigated through the implementation of the measures described in this ESMP and the Contractor's Environmental and Social Management Plan (C-ESMP), ensuring compliance with relevant national regulations and the IRP ESMF.

5. Environmental and Social Management Plan

This ESMP outlines the key measures that the Contractor and other responsible parties must implement during the subproject activities to prevent, minimize, or mitigate potential environmental and social risks and impacts. It summarizes site-specific risks identified for the reconstruction of Profilo Vocational and Technical Anatolian High School, together with the corresponding mitigation measures, monitoring indicators and frequency, assigned responsibilities, indicative costs and the overall roles of all parties involved in project implementation.

The ESMP serves as a practical tool to ensure that all project-related risks—including environmental, occupational health and safety, community health and safety, waste management, and stakeholder engagement—are managed in line with the World Bank ESF and the relevant national legislation.

The **Supervision Consultant** will be responsible for monitoring the implementation of the mitigation measures, assessing the Contractor’s environmental and social management system and performance, organizational capacity, and site-specific sub-plans. The Consultant will also review the Contractor’s ESMP (C-ESMP) and provide recommendations for improvement. The **Contractor** is obliged to prepare, adopt, and implement the Contractor’s Environmental and Social Management Plan (C-ESMP), based on this subproject’s ESMP, **prior to the commencement of civil works**, ensuring that all environmental and social commitments are fully met.

In addition to C-ESMP, the **Contractor will prepare and submit the following** sub-management plans **for review by the Supervision Consultant and approval by IPCU:**

- Waste Management Plan
- Community Health and Safety Plan
- Traffic Management Plan
- Occupational Health and Safety (OHS) Plan
- Implementation of IRP Stakeholder Engagement Plan (SEP)
- Contractor’s Labor Management Plan (in line with the Project LMP)
- Grievance Mechanism (GM) Procedures for workers and communities
- Chance Find Procedures

All sub-management plans will be submitted and approved before construction works begin and will remain in force throughout the construction period.

ISTANBUL RESILIENCE PROJECT

Table 1 Environmental and Social Management Plan

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
General for All Construction Works									
Environmental and Social (E&S) Management	<p>Contractor will prepare and submit for approval and subsequently implement its Contractor ESMP (C-ESMP). The C-ESMP should be submitted prior to the commencement of construction works and no construction activities will be carried out under the sub-project until it is reviewed and approved by the IPCU through support from the Supervision Consultant.</p> <p>The C-ESMP will include at least the following site-specific management plans:</p> <ul style="list-style-type: none"> • Occupational health and safety (OHS) management plan including risk assessment and emergency response plan (see the outline in ANNEX 6 and ANNEX 9 of the Environmental and Social Management Framework (ESMF) of the project) • Community health and safety (CHS) management plan including traffic management plan (see outline in ANNEX 7 of ESMF of the project) • Waste management Plan (see ANNEX 5 of ESMF of the project) • Chance Finds Procedures (see ANNEX 4 of ESMF of the project) • Contractor’s Labor Management Plan (to be prepared in accordance with project LMP) • Implementation of IRP Stakeholder Engagement Plan (SEP) • Grievance mechanism (GM) for both community and workers. 	X	X		All sub-management plans are approved prior to construction and implemented throughout the construction period		X		Contractor (Implementation) IPCU/Supervision Consultant
	<p>The Contractor shall hire or appoint full-time one environmental and social and one full-time OHS specialists prior to the commencement of construction works. The Contractor shall submit the CVs of specialists for approval to IPCU via Supervision Consultant. These specialists should be present at the site throughout the construction period.</p>	X	X		Relevant E&S staff are mobilized and maintained	X			Contractor (Implementation) Supervision Consultant

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
					throughout the construction period				
	<ul style="list-style-type: none"> The Contractor will prepare a training program and provide training to all its staff, before they start working on site, on basic environmental, social, health and safety (ESHS) risks associated with the proposed construction works and the workers' responsibility. The training program shall be repeated on quarterly basis. The Contractor's quarterly training program will also cover topics related to Code of Conduct (CoC) such as sexual harassment particularly towards women and children, violence, including sexual and/or gender-based violence and respectful attitudes while interacting with the local community. 	X	X		Training program approved and all relevant staff trained Training records		X		Contractor (Implementation) Supervision Consultant
Resource Efficiency and Pollution Prevention	To address the identified risks and enhance resource efficiency and pollution prevention, the following measures will be implemented: <ul style="list-style-type: none"> Ensure that all retrofitted buildings achieve at least Turkish Class C Energy Performance Certification standards (TS825) and all newly constructed buildings achieve at least Class B. Integrate renewable energy systems, such as solar panels, to reduce energy consumption and ensure operational continuity during disasters. Install water-saving systems, including low-flow toilets, efficient taps, and showerheads, and implement rainwater harvesting and greywater reuse where feasible and/or applicable. Reuse demolition materials (e.g., debris as filling material) and ensure high percentage of recycling of iron and other recyclable materials. Enhance green infrastructure by creating parks, green roofs, and vegetative buffers to manage stormwater, mitigate urban heat effects, and conserve biodiversity where feasible and/or 	X	X		Compliance with energy and water efficiency standards, proper waste and pollution management, implementation of nature-based solutions, and stakeholder feedback			X	Contractor (Implementation) Supervision Consultant

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>applicable.</p> <ul style="list-style-type: none"> Regularly monitor and evaluate the performance of nature-based solutions to ensure their long-term effectiveness. The areas where waste management will be carried out during the operation process should be determined at the planning stage. Conduct a tree survey during the planning phase to identify and document existing trees on the site, ensuring protection and conservation of mature trees wherever possible. Tree planting and the use of fire-resistant native plant species in landscaping projects can mitigate urban heat island effects while supporting ecological functions. Nature-based solutions, such as rainwater gardens and permeable surfaces, can reduce runoff, recharge groundwater, and enhance local ecosystems. 				resolution				
Air Pollution (Dust and Exhaust)	<ul style="list-style-type: none"> Minimize dust from exposed work sites by applying water on the ground regularly during the dry season. Construction debris shall be kept in a controlled area and sprayed with water mist to reduce debris dust especially during the dry season Keep stockpiles of aggregate materials covered to prevent suspension or dispersal of fine soil particles during windy days or disturbances by stray animals. In case of pneumatic drilling during excavation, dust shall be suppressed by ongoing water spraying and/or construction dust screen enclosures at the site. The surrounding environment, such as roads, shall be kept free of debris to minimize dust. Trucks transporting excavated materials or construction waste shall have their loads securely covered to prevent dust and spillage during transit. There shall be no open burning of construction or waste materials at the site. 		X		Visual inspection of air quality control measures Records of maintenance Records of complaints	X			Contractor (Implementation) Supervision Consultant

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
Noise	<ul style="list-style-type: none"> Limit construction activities to hours specified by national regulations, and coordinate with nearby communities, particularly schools, to schedule noisy tasks during times that cause minimal disturbance. During operations, equipment will be placed as far away from residential/community areas as possible. All equipment will be maintained to keep it in good working order by manufacturing maintenance procedures and installing acoustic enclosures around generators to reduce noise levels. Use when needed and feasible noise-control methods such as fences, barriers or deflectors (such as muffling devices for combustion engines or planting of fast-growing trees) Avoid the unnecessary use of alarms, horns and sirens. Minimize project transportation through community areas. Maintain a buffer zone (such as open spaces, rows of trees or vegetated areas) between the project site and residential areas to lessen the impact of noise to the living quarters. Noise measurements shall be conducted if any grievance regarding noise generation is received from the nearest receptors. If measured levels are above limit values, mitigation measures shall be enhanced in this respect, i.e., installing acoustic barriers for mechanical equipment, limiting the hours of operation for specific pieces of equipment or operations, etc. 		X		Visual inspection of noise control measures Records of complaints	X			Contractor (Implementation) Supervision Consultant
Health and Safety OHS-related risks due to unsafe practices and hazards at work sites such as	When planning activities, discuss steps to avoid people getting hurt. It is useful to consider: <ul style="list-style-type: none"> Construction place: Are there any hazards that could be removed or should warn people about? The people who will be taking part in construction: Do the participants have adequate skill and physical fitness to perform 	X			Visual inspection Employee records	X			Contractor (Implementation) Supervision Consultant

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
work at height, rotating and moving equipment, electrical safety, working with hazardous material, etc.	<p>their work safely?</p> <ul style="list-style-type: none"> • The equipment: Are there checks you could do to make sure that the equipment is in good working order? Do people need any particular skills or knowledge to enable them to use it safely? • Electricity Safety: Do any electricity good practices such as the use of safe extension cords, voltage regulators and circuit breakers, labels on electrical wiring for safety measures, awareness on identifying burning smells from wires, etc. apply at the site? Is the worksite stocked with voltage detectors, clamp meters and receptacle testers? 				Equipment				
	<ul style="list-style-type: none"> • Appropriate signposting of the construction sites will inform workers of key rules and regulations to follow. • The contractor’s OHS specialist will provide a brief daily toolbox talk to the construction workers on ESHS risks associated with the construction activity that will be carried out on that particular day.. • The Contractor will ensure a safe working environment for the workers and before construction activities will supply appropriate personal protective equipment (PPE) in line with international best practice and Turkish Legislation (hard hats, gloves, dust masks, goggles, harnesses and safety boots, etc.). • All activities will be implemented in line with both the Law on Occupational Health and Safety (Official Gazette No: 28339, dated June 30, 2012) and its relevant regulations and also with the World Bank Group EHS Framework. • The Contractor will immediately notify the IPCU (through supervision consultants) about any serious incident which may have significant adverse effects on the environment, the affected communities, the public or workers. Then, IPCU will notify the World Bank about any serious incident in 48 hours and send an incident investigation report together with the root-cause analysis 		X		<p>Visual inspection of control measures</p> <p>OHS records</p> <p>Employee records</p> <p>Incident statistics and records, including near misses</p> <p>Records of worker’s complaints</p>	X			<p>Contractor (Implementation)</p> <p>Supervision Consultant</p>

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>and corrective action plan no later than 10 days to the World Bank.</p> <ul style="list-style-type: none"> • Keep the worksite clean and free of debris on a daily basis. • The first aid kit should be equipped with bandages, antibiotic creams, etc. or delivered to health institutions. • Following safety guidelines for the storage, transport, and distribution of hazardous materials aiming to minimize the potential for misuse, spills, and accidental human exposure. • Keep corrosive fluids and other toxic materials in properly sealed containers for collection (considering its MSDS) and disposal in properly secured areas. • Ensure structural openings are covered/protected adequately. • Secure loose or light material that is stored on roofs or open floors. • Keep hoses, power cords, welding leads, etc. from laying in heavily travelled walkways or areas. • During heavy rains or emergencies of any kind, suspend all work. • Follow the below measures for construction involving work at height: <ul style="list-style-type: none"> • Do as much work as possible from the ground. • Do not allow people with the following personal risks to perform work at height tasks: eyesight/balance problem; certain chronic diseases – such as osteoporosis, diabetes, arthritis or Parkinson’s disease; certain medications – sleeping pills, tranquilizers, blood pressure medication or antidepressants; recent history of falls – having had a fall within the last 12 months, etc. • Only allow people with sufficient skills, knowledge and experience to perform the task. • Check that the place (e.g., a roof) where work at height is to be undertaken is safe. 								

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<ul style="list-style-type: none"> Take precautions when working on or near fragile surfaces. Clean up oil, grease, paint, and dirt immediately to prevent slipping in accordance with Emergency Response Plan; and Provide fall protection measures e.g. safety harness, and simple scaffolding/guard rail for works over 4 meters from the ground. The contractor shall hire trained operators for the safe operation of specialized construction's vehicles 								
<p>Community Health and Safety</p> <p>Community health and safety risks associated with construction activities, including health issues arising from exposure to waste, stagnant water, wastewater, particulate matter, and construction workers, as well as traffic and road-related risks caused by increased traffic volume and the movement of heavy-duty vehicles due to inadequate construction and traffic management.</p>	<ul style="list-style-type: none"> Rope off construction area and secure materials stockpiles/ storage areas from the public and display warning signs including at unsafe locations. Do not allow the entrance of unauthorized person in construction areas. Regularly drain stagnant water from construction areas to prevent the breeding of mosquitoes and other disease vectors. Use covered and sealed storage for wastewater to prevent leaks and odors, while maintaining safe drainage systems to avoid contamination of nearby water bodies. Provide clean and well-maintained sanitation facilities for workers, including toilets and washing stations. The construction site security personnel must be trained and officially certified. Control the driving speed of vehicles particularly when passing through a community or nearby school, health center or other sensitive areas. If vulnerable pedestrians or facility users are present in the vicinity, include traffic safety personnel to direct traffic during school hours, if needed. The project site must be lit during the night. The surrounding construction area should be kept clean, without waste disposed of there. The broken glass should be cleaned 		X		<p>Visual inspection of control measures</p> <p>Traffic accident records</p> <p>Records of complaints</p>	X		<p>Contractor</p> <p>Consultant (Supervision)</p>	

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>immediately to avoid any fires.</p> <ul style="list-style-type: none"> • Following safety guidelines for transportation of hazardous materials to the site aiming to minimize the potential for spills and accidental human exposure due to traffic accidents. • Effective communication systems are needed to inform communities about project activities, potential risks, and emergency procedures. • Regular maintenance such as periodical control of vehicles to minimize potentially serious accidents caused by equipment malfunction or premature failure. • The public will be informed about the work to be carried out, including the measures taken regarding communicable diseases relating to labor influx and -post-disaster context (i.e., infectious disease outbreaks), using appropriate communication tools and methods (e.g., online/virtual and/or physically) in areas accessible to all stakeholders (including work sites). • In case of any epidemic or pandemic / communicable disease, including infectious disease outbreaks, the guidance, guidelines, and recommendations to be provided by the Ministry of Health, the Ministry of Family and Social Services, the Ministry of Labor and Social Security, and the World Health Organization (WHO) will be followed, and all relevant measures will be taken for both employees and workplaces in terms of OHS and CHS. In addition, all construction works will follow the World Bank guidelines to minimize the risk of infectious disease outbreaks transmission during the execution of civil works. • Include evacuation protocols, first aid training, and clear communication strategies in the ERP to protect community health and safety. • Any traffic diversions should take into account the needs of disabled persons. 								

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<ul style="list-style-type: none"> The Contractor will ensure the construction site is properly secured and construction-related traffic regulated properly (including proper route planning). This will include but not be limited to: Signposting, warnings, barriers, and traffic diversions: the site will be visible, and the public warned of all potential hazards. Traffic management system and staff training, especially for site access and near-site heavy traffic. Provision of safe passages and crossings for pedestrians where construction traffic interferes. Adjustment of working hours to local traffic patterns, e.g. avoiding major transport activities during rush hours or times of livestock movement. Active traffic management by trained and visible staff at the site, if required for a safe and convenient passage for the public. 								
<p>Water Quality and Wastewater: Water pollution in nearby surface waters due to wastewater/waste generated at the construction area due to construction activities</p>	<ul style="list-style-type: none"> The site will establish appropriate erosion and sediment control measures such as e.g. hay bales and/or silt fences to prevent sediment from moving off-site and causing excessive turbidity in nearby surface waters. Minimize storage or disposal of generated wastewater on the site. Temporary or final waste disposal and wastewater discharge without treatment near/in surface waters is strictly forbidden to prevent possible adverse impacts on surface waters. No soiled materials, solid wastes, toxic or hazardous materials should be stored in, poured into or thrown into water bodies for dilution or disposal. Construction vehicles and machinery will be washed only in designated areas where runoff will not pollute natural surface waters. Wastewater generated at the construction site will be connected to the sewerage system, if possible, and approved by local authorities. If this is not possible, it will be deposited in the septic 		X		Visual inspection of control measures Septic tank effluent disposal records (if any) Effluent quality measurement records (if any) Records of complaints	X			Contractor <i>(Implementation)</i> Supervision Consultant

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>tank that will be impervious, in accordance with “Regulation on Pit Opening Where Sewer System Construction is not Applicable” published in Official Gazette No: 13783 dated 19.03.1971. Toilets with temporary septic tank might be used for this purpose as well. Septic tank effluent will be removed periodically by sewage trucks, and disposal will be provided within the scope of the protocol to be made with the relevant municipality that has a licensed wastewater treatment plant (WWTP). The Protocol will be submitted to the IPCU.</p> <ul style="list-style-type: none"> • Activities should not affect the availability of water for drinking and hygienic purposes. • The flow of natural waters should not be obstructed or diverted in another direction, which may lead to the drying up of river beds or flooding of settlements. • Separate concrete works in waterways and keep concrete mixing separate from drainage leading to waterways. 								
<p>Soil and Groundwater Quality: Soil and groundwater pollution due to improper waste management and accidental spills, and soil erosion</p>	<ul style="list-style-type: none"> • Apply the mitigation measures specified in the “Solid and Hazardous Waste” section for proper waste management. Residual (left out) concrete in concrete mixers will not be allowed to wash out into the construction site, its vicinity, or access roads of construction sites. Related trainings will be provided to concrete mixer drivers. • Hazardous and chemicals and materials will be secured in a designated storage area to prevent spillage and tip-over. • Semi-used chemical-containing containers will have lids and lids will be tightened while they are not in use. • In case of a spill of any hazardous material or hazardous wastes, spill prevention methods mentioned in ERP will be put in place in order to limit the exposure area. Workers who might intervene in such incidents should have relevant trainings on emergency response to spills. 		X		<p>Visual inspection of control measures Incident records Training records Records of complaints</p>	X			<p>Contractor <i>(Implementation)</i> Supervision Consultant</p>

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<ul style="list-style-type: none"> • Proper spill kits will be placed at appropriate locations in the construction area. • Schedule construction during the dry season, as appropriate. • Contour and minimize the length and steepness of slopes. • Cover with topsoil and re-vegetate (plant grass, fast-growing plants/bushes/trees) construction areas quickly once work is completed. 								
<p>Waste Management EHS risks due to inappropriate management of waste generated due to construction activities (such as construction demolition wastes, hazardous waste, biodegradable waste, recyclable waste, non-hazardous waste, etc.)</p>	<ul style="list-style-type: none"> • Excavation soil, construction and demolition waste Dumping Permit must be obtained from the Municipality. • Excavation waste will be re-used for backfilling purposes as much as possible and recovery and other re-use options will be considered as appropriate (except asbestos or asbestos-containing waste). • Recycling and reusing materials during demolition and construction reduces demand for raw natural resources, indirectly supporting sustainable management practices. • The excess excavation waste shall be transported and disposed of separately by licensed transport vehicles to existing licensed excavation waste storage area(s), identified by the relevant governmental authorities, in the district/region. • On-site storage of wastes prior to final disposal (including earth dug for foundations) should be at least 300 meters from rivers, streams, lakes and wetlands. • After each construction site is decommissioned, all debris and waste shall be cleared. • Keep the records of waste generation and disposal. 	X	X		Visual inspection of control measures Waste generation and disposal records Training records Records of complaints	X			Contractor (Implementation) Supervision Consultant
	<ul style="list-style-type: none"> • Manage wastes in accordance with the waste management hierarchy (prevent, reduce, reuse, recycle, recover, dispose) and train personnel to raise awareness on waste management. • Temporarily storage on site of all hazardous or toxic substances 								

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>will be in safe containers labelled in line with Material Safety Data Sheet (MSDS), with details of composition, properties, and handling information.</p> <ul style="list-style-type: none"> • Segregate waste as recyclable, hazardous and non-hazardous waste. • Non-hazardous wastes, inert and biodegradable wastes and also recyclables must be collected separately, and special attention must be paid to prevent hazardous wastes in leak-proof container to prevent spillage and leaching in case of mixing with other types of waste. • Collect, store and transport waste to appropriately designated /controlled licensed disposal areas/facilities (such as excavation waste storage areas, sanitary landfills, recycling/recovery facilities, etc.). Submit an official letter to IPCU stating that these wastes will be accepted at licensed sites • Temporary waste storage area (to be established at the construction area) should be on impermeable ground, covered with a roof, and equipped with a suitable drainage system, proper spill kits and appropriate firefighting equipment. Wastes shall be temporarily stored in this area in separate compartments (labelled with waste codes) according to their types in order not to react with each other. Hazardous wastes shall be stored in the temporary waste storage area for a maximum of six (6) months and non-hazardous wastes for a maximum of one year. • Hazardous waste shall be transferred to a licensed disposal facility via licensed waste transportation companies, and recyclable wastes to a relevant licensed recycling/recovery facility. All protocols and waste logs shall be submitted to the IPCU. • Train workers on correct transfer and handling of fuels and other substances and require the use of gloves, boots, aprons, eyewear 								

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	and other protective equipment for protection in handling highly hazardous materials.								
<p>Stakeholder Engagement and Grievance Mechanism</p> <p>Construction-related complaints and temporary disruption to the local community including eligible property owners</p>	<ul style="list-style-type: none"> Follow the relevant measures suggested in the SEP. Early liaison and effective communication shall be carried out with people who may be affected by the work of the contractor and supervision consultant. Implementation of a program of ongoing liaison and respect for the local environment and residences shall be formed The supervision consultant will appoint a dedicated person(s) accountable for community liaison who will be focused on engaging with the community to provide the appropriate information and to be the first line of response to resolve issues of concern. The Project Grievance Mechanism shall be implemented through the opening and closing of forms and complaints. The names and contact telephone numbers and e-mail addresses of all site personnel with responsibilities for both supervision and management of the works will be displayed on the site information boarding. Once planning consent has been obtained, formal contact will be established with the mukhtar of the neighborhood and those who could potentially be affected by the construction will be informed via mukhtar. This will include consultation with relevant E&S risk management instruments and identifying any particularly sensitive times of the day. Outside normal working hours, security personnel will act as the main point of contact via a dedicated phone number. Security will alert the person(s) accountable for liaison if necessary (available 24 hours). All workers will sign/commit to and be trained on the Code of Conduct to manage the potential adverse impacts on social 	X	X		Records of complaints Stakeholder engagement records	X		<p>IPCU</p> <p>Contractor (Implementation)</p> <p>Supervision Consultant</p>	

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>cohesion and Sexual Exploitation and Abuse/Sexual Harassment (SEA/SH) risks.</p> <ul style="list-style-type: none"> Any complaints will be logged, fully investigated, and responded to quickly, advising what action has been taken. Complaints will be registered and reported to the Contractor, Training Consultant, Supervision Consultant and also IPCU. Public notice boards will be established at site entrances during the Planning and Construction phases, providing relevant contact details of the for liaison including environmental matters. 								
<p>Labor and Working Conditions: Risks associated with potential labor influx (such as child labor risks, gender-based violence and harassment, human rights risks, etc.) and other labor issues</p>	<ul style="list-style-type: none"> Follow the relevant measures in Labor Management Plan (LM Plan) to be prepared by the Contractor in accordance with project LMP. Workers will be provided with information and documentation that is clear and understandable regarding their terms and conditions of employment such as their rights under national labor and employment law (which will include any applicable collective agreements). Workers will be paid on a regular basis as required by national law and project LMP. Workers will be provided with adequate periods of rest per week, annual holiday and sick, maternity and family leave, as required by national law and project LMP. Workers will receive written notice of termination of employment and details of severance payments in a timely manner. Workers will be employed on the principle of equal opportunity and fair treatment, and there will be no discrimination with respect to any aspects of the employment relationship. Project workers, including specific groups of workers, such as women, people with disabilities and migrant workers will be provided with appropriate measures of protection and assistance 		X		<p>Visual inspection of control measures</p> <p>Health records</p> <p>Employee records</p> <p>Training records</p> <p>Records of worker's complaints</p>	X		<p>Contractor (Implementation)</p> <p>Supervision Consultant</p>	

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>in line with ESS2 of WB ESF. This process will be executed in accordance with the project LMP.</p> <ul style="list-style-type: none"> • Workers are allowed to participate, or seek to participate, in workers' organizations and collective bargaining or alternative mechanisms. • Children under the minimum age of 18 will not be employed or engaged by the Contractor in connection with this sub-project. • Forced labor, which consists of any work or service not voluntarily performed that is exacted from an individual under threat of force or penalty, will not be used in connection with this sub-project. • Prior to commencement of any activities at the project site, a worker's GM will be established by the Contractor at the construction site for all workers to raise workplace concerns. Contact details of the worker's GM will be provided to workers during the induction training. • All workers will receive training about their rights under national labor and employment law and regarding the GM upon recruitment and before the implementation of the work. • Code of Conduct will be shared with project workers during employment. All workers are obliged to comply with the Code of Conduct and sign relevant documentation at the time of employment. • Movement in and out of the construction site will be controlled, and unauthorized access to the site will be prevented. • Contractor will confirm that workers are fit for work before they start work, paying special attention to workers with underlying health issues or who may be otherwise at risk. • The Contractor shall provide information and awareness of communicable diseases to workers. • The Contractor shall arrange safe drinking water, adequate toilet 								

ISTANBUL RESILIENCE PROJECT

Potential Risks and Impacts	Proposed Mitigation Measures	Phase			Indicators for monitoring	Frequency of Monitoring			Responsibility for implementation and monitoring
		Planning	Construction	Operation		Continuous	Monthly	Quarterly	
	<p>facilities for both genders, accommodation, rest and dining areas for the workers.</p> <ul style="list-style-type: none"> The Contractor shall provide a first aid kit with bandages, antibiotic cream, etc. or health care facilities, and shall identify and train an adequate number of workers to provide first aid during medical emergencies. 								
<p>Cultural Heritage</p> <p>Chance Find</p>	<ul style="list-style-type: none"> Effective communication with local authorities, heritage organizations, and the community will ensure proper handling of any cultural heritage No disturbance of cultural or historic sites. If encountered with any cultural heritage/assets during construction works (especially excavation and earthworks) apply the chance finds procedure (see Annex 4 of ESMF of the project). 	X	X		Chance finds records		X	<p>IPCU</p> <p>Contractor <i>(Implementation)</i></p> <p>Supervision Consultant</p>	
<p>Biodiversity:</p> <p>Potential risks to flora and fauna due to construction activities and improper waste management</p>	<ul style="list-style-type: none"> According to Planned Areas Development Regulations (published in the Official Gazette dated July 03, 2017, and numbered 30113 and Attachment: RG-31/12/2022-32060) for residential, trade, tourism, education, worship, health, and sports parcels: 1 tree per 30 m² of area outside the building footprint. If planting on the parcel is not feasible, trees must be planted in designated public areas per zoning plans Tree planting and the use of fire-resistant native plant species in landscaping projects can mitigate urban heat island effects while supporting ecological functions 		X		<p>Tree plantation records</p> <p>Screening</p> <p>Visual inspection of control measures</p>		X	<p>Contractor <i>(Implementation)</i></p> <p>Supervision Consultant</p>	

ISTANBUL RESILIENCE PROJECT

6. Roles and Responsibilities

The activities to be carried out under the Site-Specific Environmental and Social Management Plan (ESMP) and the parties responsible for these activities are presented in Table 2.

Table 2 Roles and Responsibilities

Responsible Party	Roles and Responsibilities
IPCU	<ul style="list-style-type: none"> • Hire/appoint one environmental, one social, and one OHS specialist to ensure the effective management and monitoring of environmental, social, and OHS risks in compliance with project requirements. • Through its environmental, social and OHS specialists; <ul style="list-style-type: none"> - Coordinate closely with local authorities, contractors, and community leaders to ensure alignment with project goals, environmental and social requirements, and stakeholder expectations. - Develop and maintain a centralized database to track the implementation of environmental and social mitigation measures, grievances, and monitoring data, ensuring accessibility and up-to-date information for reporting to the World Bank and other stakeholders. - Provide oversight, support, and quality control for field staff and contractors working on environmental and social risk management. - Ensure subprojects are screened against the Exclusion List (Table 5 of ESMF of the project). - Prepare E&S Screening Forms for each of the subprojects and submit them to the WB for approval. - For activities requiring ESMPs, prepare site-specific ESMPs by customizing the project level ESMP (Annex-3 of ESMF of the project) and submit at least first five (5) ESMPs for prior review and no objection by the WB for disclosure and consultation purposes. - Disclose and consult upon the WB cleared version of the site specific ESMPs prior to the initiation of the tendering process. Following the consultations, update the site-specific ESMPs to incorporate the outcomes of the consultations and submit it to the WB’s clearance for tendering purposes. - Ensure all tender, bidding and contract documents include relevant E&S management provisions and references to relevant E&S instruments (i.e. ESMPs, SEP, LMP, etc.). - Ensure site-specific ESMPs are annexed to the relevant tendering documents. • Train central and field staff, as well as contractors, on implementing the ESMF and associated plans. • Prior to commencement of civil works, review and approve C-ESMP, LM Plan and E&S sub-management plans to be prepared by the contractor and ensure their implementation throughout the duration of subproject implementation. <ul style="list-style-type: none"> - Visit and monitor E&S performance of construction sites monthly and maintain all correspondences with governmental authorities. - Establish and maintain a grievance mechanism and resolve complaints at all levels. - Notify the World Bank of any serious E&S incidents within 48 hours and provide incident reports with root cause analysis and corrective actions within 10 days. - Oversee the implementation and monitoring of environmental and social mitigation measures.

ISTANBUL RESILIENCE PROJECT

	<ul style="list-style-type: none"> - Maintain documentation of progress and prepare consolidated reports for submission to the World Bank on a quarterly basis.
<p>Supervision Consultants (Construction)</p>	<ul style="list-style-type: none"> • Overseeing daily implementation and monitoring of environmental, social and health and safety (ESHS) mitigation measures, and report progress and ESHS performance of the sub-projects to the implementing IPCU monthly. • Ensure contractors comply with legislation, site-specific ESMPs and relevant E&S sub-management plans. • Maintain one OHS specialist and one Environmental and Social Specialist with relevant certification and/or experience in charge of E&S management, in line with the implementation arrangements defined in the Supervision Consultant’s Terms of Reference and the specific needs of the sub-project. • Daily on-site monitoring of the implementation of E&S mitigation measures will be carried out by the Contractor’s designated E&S personnel and verified through regular site visits by the Supervision Consultant. The IPCU will exercise oversight through review of site records, supervision reports, and monthly consolidated E&S performance reports submitted in Section 5.1.c. of IRP ESMF. • Prior to commencement of any construction works on site, in coordination with IPCU, review and approve C-ESMP, LM Plan and E&S sub-management plans prepared by the contractor and ensure their implementation throughout the duration of subproject implementation. All approved documents will be submitted to IPCU within 5 business days. Any deficiencies or non-compliances identified by IPCU will be communicated to the contractor by the supervisor, and the contractor will be required to address them within 15 business days. • Provide training to contractors on E&S and OHS measures. • In close collaboration with the IPCU, ensure effective implementation of the SEP at the site level. • When/where relevant, address grievances received from the stakeholders. • Inform the IPCU about serious E&S (including OHS) incidents immediately.
<p>Contractors</p>	<ul style="list-style-type: none"> • Prior to commencement of any civil works prepare C-ESMP, LM Plan and relevant E&S sub-management plans and submit these documents to the IPCU for their review and approval. • Maintain full-time OHS specialist and one full-time Environmental and Social Specialist with relevant certification and/or experience in charge of E&S management throughout the construction period, in line with the staffing arrangements defined in the IRP ESMF and reflected in Table 1 and Table 3 of this ESMF. • Ensure implementation of and compliance with the Project’s environmental and social mitigation measures as outlined in the C-ESMP, LM Plan and relevant E&S sub-management plans, and contract documents, and ensure adherence to national and local legislation. • Address construction-related grievances as per the GM procedure described in the Project SEP and escalate unresolved issues to Supervision Consultants/IPCU immediately. • Notify Supervision Consultant/IPCU through of any serious E&S incidents immediately. • Monitor site activities on daily basis and report on the E&S performance to supervision consultants/IPCU on monthly basis. • Provide regular training and capacity-building sessions for the workforce on, but not limited to, E&S risk management (labor rights and obligations under the LMP, Stakeholder engagement practices based on SEP requirements, ERP, OHS plan, community safety and traffic management plan, waste management plan, Code of Conduct, etc.)

ISTANBUL RESILIENCE PROJECT

7. Capacity Building and Training

The Contractor shall design and implement a structured training program for all project workers and relevant stakeholders. At a minimum, the following trainings will be delivered and repeated periodically:

- Environmental and Social Management & Occupational Health and Safety Induction Training – for all workers before starting site activities.
- Site Access and Orientation Training – including induction for visitors and orientation for newly mobilized workers.
- Traffic and Pedestrian Safety Training – covering movement of heavy vehicles, safe pedestrian crossings, and community-sensitive driving practices.
- Code of Conduct Training – addressing respectful workplace practices, sexual harassment prevention, and interaction with local communities.
- Gender-Based Violence (GBV), Sexual Exploitation and Abuse/Sexual Harassment (SEA/SH) Training – focusing on awareness, prevention, and survivor-centered response.
- Waste Management Training – segregation, storage, transport, and safe handling of construction and hazardous wastes.
- Emergency Preparedness and Response Training – including fire safety, evacuation drills, spill response, and first aid.
- Incident and Accident Reporting Training – procedures for immediate notification, root cause analysis, and corrective actions.
- Grievance Mechanism (GM) Training – how workers and community members can access and use the GM system.
- Stakeholder Engagement and Communication Training – for E&S staff and supervisors to ensure meaningful interaction with local communities.

The Contractor is responsible for organizing and financing these trainings, either internally or through external certified providers.

ISTANBUL RESILIENCE PROJECT

8. Implementation Schedule and Cost Estimates

An indicative cost schedule has been prepared for the mitigation and capacity building measures to be implemented throughout the Project.

Table 3 Indicative ESMP Implementation Budget¹

Activity/Cost Item	Potential Cost (USD)
Full-time Environmental, Social & OHS Consultants	80.000,00 USD
Monitoring / Site Visits / C-ESMP Preparation	10.000,00 USD
Trainings, Awareness, Capacity Building	15.000,00 USD
Implementation of SEP & ESMP Measures	10.000,00 USD
Communicable Disease Prevention	5.000,00 USD
TOTAL	120.000,00 USD

¹ These indicative costs are covered under the Project budget and provided for planning purposes. Contractors shall reflect their own implementation costs in their bids.

ISTANBUL RESILIENCE PROJECT

9. Stakeholder Engagement and Grievance Mechanism

Stakeholder engagement is an inclusive and continuous process to be carried out throughout the Project lifecycle. It supports the establishment of strong, constructive, and responsive working relationships and is essential for the successful management of the Project's environmental and social (E&S) risks and impacts.

Within the scope of the Istanbul Resilience Project (IRP), a Stakeholder Engagement Plan (SEP) has been prepared to guide structured engagement with stakeholders, including the management and users of potentially affected or directly benefiting buildings. The SEP facilitates the management of stakeholder expectations and risks, helps reduce potential conflicts and delays, and ensures early, frequent, and transparent communication.

The SEP also establishes accessible and inclusive tools for affected people to raise concerns, suggestions, and grievances, enabling the Istanbul Project Coordination Unit (IPCU) and other responsible institutions to respond and manage issues effectively.

During project preparation, consultation meetings were organized with representatives from public institutions, local authorities, school administrations, teachers, parents, and community members. In these meetings, the Project's financing sources, objectives, components, and eligibility criteria for building selection were presented. The concerns, questions, and feedback of participants were documented and reflected in the SEP.

Following the disclosure of the draft version of this site-specific ESMP on 24 June 2026, an information and public consultation meeting was held on 2 July 2026 at 10:00 in relation to the Kağıthane Profilo Vocational and Technical Anatolian High School subproject. The meeting took place at Kağıthane Anatolian High School, located at Çağlayan Mahallesi, Ayazma Caddesi No:22, Metro Market Karşısı, Kağıthane, Istanbul, and was organized in line with the stakeholder engagement and information disclosure standards of the IRP.

The invitation to the meeting was formally conveyed through the Provincial Directorate of National Education, as the beneficiary institution of the subproject, via an official letter presented in Annex 6. In addition, a public announcement was made through the IPCU's official website to ensure broader stakeholder awareness and participation, as shown in Annex 7.

The consultation meeting was attended by school representatives and teachers. A total of 38 participants attended the meeting, comprising 10 women and 28 men, based on the participant list prepared for the event. As the meeting venue was located within a school premises and was accessible to the invited participants, no specific transportation arrangements were required. The minutes of the meeting are provided as Annex 8 to this site-specific ESMP.

During the meeting, participants were informed about the IRP and the key environmental and social aspects of this site-specific ESMP. In addition, the design consultant presented the project visuals, including the architectural design, school access and circulation arrangements, emergency evacuation routes, green areas, landscaping arrangements, indoor and outdoor social spaces, and rooftop use. The presentation also covered the technical and resilience-enhancing features of the school building, including energy efficiency measures, photovoltaic solar panel installation, and infrastructure arrangements intended to support the functionality, safety, and sustainability of the school. The presentation materials used for the subproject-specific ESMP briefing and the Kağıthane Profilo Vocational and Technical Anatolian High School Reconstruction Project Design presentation are provided in Annex 9 and Annex 10, respectively. Photographs taken during the information and consultation meeting are presented in Annex 11.

ISTANBUL RESILIENCE PROJECT

Participants raised questions, comments, and suggestions mainly related to school access and circulation arrangements, post-construction landscaping and tree planting, indoor and outdoor social spaces, construction quality and supervision, secure installation of building equipment and fixtures, electrical and communication infrastructure, compliance with the Ministry of National Education's FATİH Project requirements, durable and easy-to-maintain building materials, sanitary fixture preferences, perimeter boundary fencing, campus security, and rooftop use.

In response, the design consultant explained the main entrance, circulation scheme, and emergency evacuation routes, and demonstrated the designated green spaces and tree planting zones on the current landscape plans. It was also explained that the entrance halls, foyers, and indoor central atriums are designed to function as multi-use social and recreational gathering areas. Regarding construction quality and supervision, IPCU explained that construction activities will be monitored by IPCU site engineers and the E&S team, and that all materials will be required to comply with the relevant technical specifications. The Defect Liability Period and provisional acceptance framework were also explained.

Regarding the secure installation of building equipment and fixtures and reliable electrical and communication infrastructure, it was explained that the building design incorporates a raised-floor system to improve the protection and accessibility of electrical and communication infrastructure. In relation to the FATİH Project requirements, it was explained that the new school design has been prepared to accommodate current MoNE digital infrastructure standards, and that similar systems have been successfully implemented in previous projects without implementation or operational issues.

Regarding material selection and sanitary fixtures, it was explained that material selection is based on the project technical specifications and international procurement requirements. In relation to perimeter boundary fencing, it was clarified that the perimeter security framework consists of a 1.5-meter reinforced concrete boundary wall, with additional wire mesh fencing above the wall to enhance site security. Regarding rooftop use, it was explained that the roof is designed to accommodate photovoltaic solar panels to improve energy efficiency.

Overall, no objections to the subproject were expressed, and stakeholders demonstrated general support for the reconstruction, particularly acknowledging the importance of appropriate access and circulation arrangements, post-construction landscaping, adequate social spaces, construction quality and supervision, reliable infrastructure, durable materials, campus security, and energy efficiency measures. Construction activities will be monitored during the project duration.

Attendance sheets and participant records were collected with wet signatures and are securely archived by the IPCU in compliance with the Law on the Protection of Personal Data (KVKK). These records are retained solely for project documentation, monitoring, and audit purposes and are not publicly disclosed.

A dedicated Grievance Mechanism has been established to ensure that any grievances or requests related to subprojects financed under the IRP —raised by contractors, supervision staff, building users, or the community—are addressed in a timely, effective, and fair manner. The GM operates through multiple accessible channels, as detailed below:

Project-Specific Channels (IPCU)

- **Hotline (phone):** +90 (216) 505 55 00 (during working hours)
- **E-mail:** info@ipkb.gov.tr
- **Postal Address:** Istanbul Project Coordination Unit (IPCU), Kısıklı Mah. Alemdağ Yan Yolu Cad. No:6, 34692 Üsküdar/İstanbul
- **In-person:** Stakeholders may visit IPCU offices during working hours
- **Online Grievance/Suggestion Form:** <https://www.ipkb.gov.tr/sikayet-formu/>
- **Social Media Channels:**
 - Twitter: <https://x.com/ipkbgovtr>

ISTANBUL RESILIENCE PROJECT

- Facebook: <https://www.facebook.com/ipkbgovtr>
- Instagram: <https://www.instagram.com/ismepipkb/>
- LinkedIn: <https://www.linkedin.com/company/ipkb>
- YouTube: <https://www.youtube.com/user/IPKBirimi>
- **On-site Complaint/Suggestion Boxes:** These will be established at project sites and IPCU offices, once activities commence on site, ensuring anonymity and confidentiality.

National Channels

- **CİMER (Presidency's Communication Center):**
 - Website: www.cimer.gov.tr
 - Call Center: 150
 - Phone: +90 (312) 590 20 00
 - Fax: +90 (312) 473 64 94
 - Mail: Presidency of the Republic of Türkiye Directorate of Communications
 - In-person: Through provincial/district governorates and ministries
- **YİMER (Foreigners Communication Center):**
 - Website: www.yimer.gov.tr
 - Call Center: 157
 - Phone: +90 (312) 157 11 22
 - Fax: +90 (312) 920 06 09
 - E-mail: yimer@goc.gov.tr
 - In-person: At Directorate General of Migration Management offices
- **Istanbul Metropolitan Municipality (IMM) – White Desk (Beyaz Masa):**
 - Hotline: 153 (within Istanbul)
 - Online: <https://beyazmasa.ibb.gov.tr/>

World Bank Channels

- **World Bank Grievance Redress Service (GRS):**

Project-affected people may submit complaints directly to the GRS if they believe they are adversely affected by a World Bank-financed project.

- Website: <https://www.worldbank.org/en/projects-operations/products-and-services/grievance-redress-service>

- **World Bank Inspection Panel:**

Communities and individuals who believe that they are or may be harmed by a project due to the World Bank's non-compliance with its policies may submit a complaint to the Inspection Panel. The Panel independently determines whether harm has occurred and communicates directly with the Bank.

All grievances received through these channels will be recorded, tracked, and responded to in accordance with the Project's Grievance Mechanism Procedures. Roles and responsibilities for managing grievances are described in detail in Section 7 of the SEP.

ISTANBUL RESILIENCE PROJECT

10. Contractor's Reference Documents

The Contractor is expected to utilize all Environmental and Social (E&S) documents prepared under the Istanbul Resilience Project (IRP). Following contract award, the Contractor shall further develop and customize this site-specific Environmental and Social Management Plan (ESMP), which has been prepared in outline by the IPCU experts for the respective subproject.

In addition to the C-ESMP, the Contractor shall prepare and submit site-specific sub-management plans as defined in Section 5 of this ESMP, based on the templates provided in the ESMF annexes.

These plans shall be prepared and submitted to the IPCU for review and approval prior to the commencement of construction activities.

All relevant template documents can be accessed through the IRP Environmental and Social Management Framework (ESMF) and its annexes (*see IRP ESMF*), which serve as reference documents for the Contractor.

11. Review and Approval

PREPARED BY: Hande GÜLCAN IPCU - Environmental Engineer, MSc Date: 24/06/2026	
REVIEWED BY: Ashhan AL IPCU – Urban Planner/Social Specialist Date: 24/06/2026	APPROVED BY: Burak REİS IPCU - E&S Management Team Leader Date: 24/06/2026

ISTANBUL RESILIENCE PROJECT

ANNEXES

ISTANBUL RESILIENCE PROJECT

Annex 1. Site Photographs



ISTANBUL RESILIENCE PROJECT



Photos 1-2-3-4: The project site (newly designated parcel) photographs and its surroundings from different perspectives

ISTANBUL RESILIENCE PROJECT

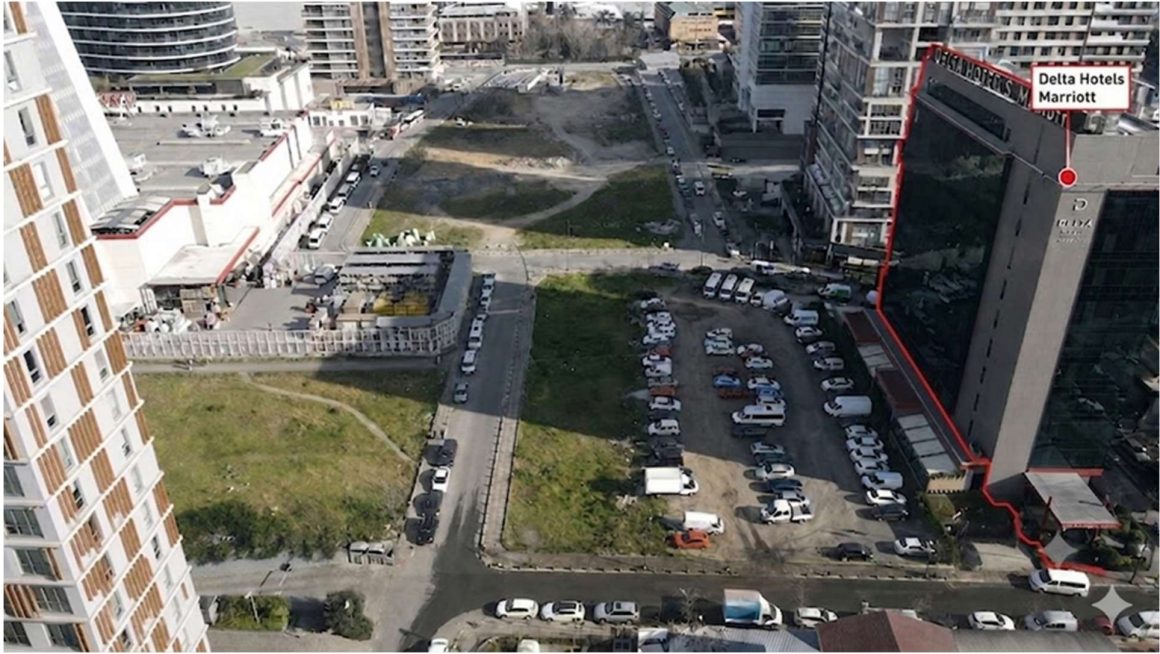


Photo 5: The hotel adjacent to/near to the project site



Photo 6: Sensitive receptors (school and mosque) near the project site

ISTANBUL RESILIENCE PROJECT

Annex 2. Aerial View of the Project Site and Surroundings



Photo 1: Location of the new project site (Block 7035, Plot 3)

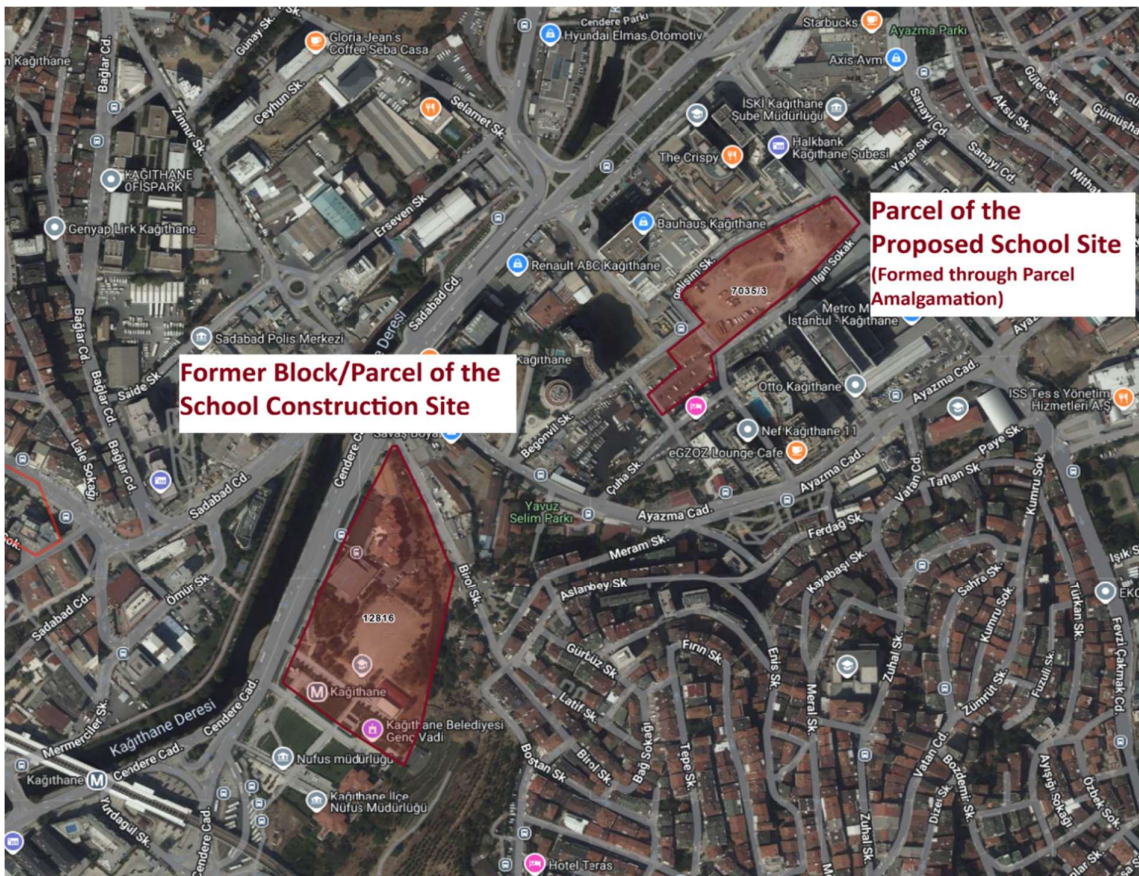


Photo 2: Existing (Block 0, Plot 12816) and proposed project (Block 7035, Plot 3) parcels for the school construction site

ISTANBUL RESILIENCE PROJECT

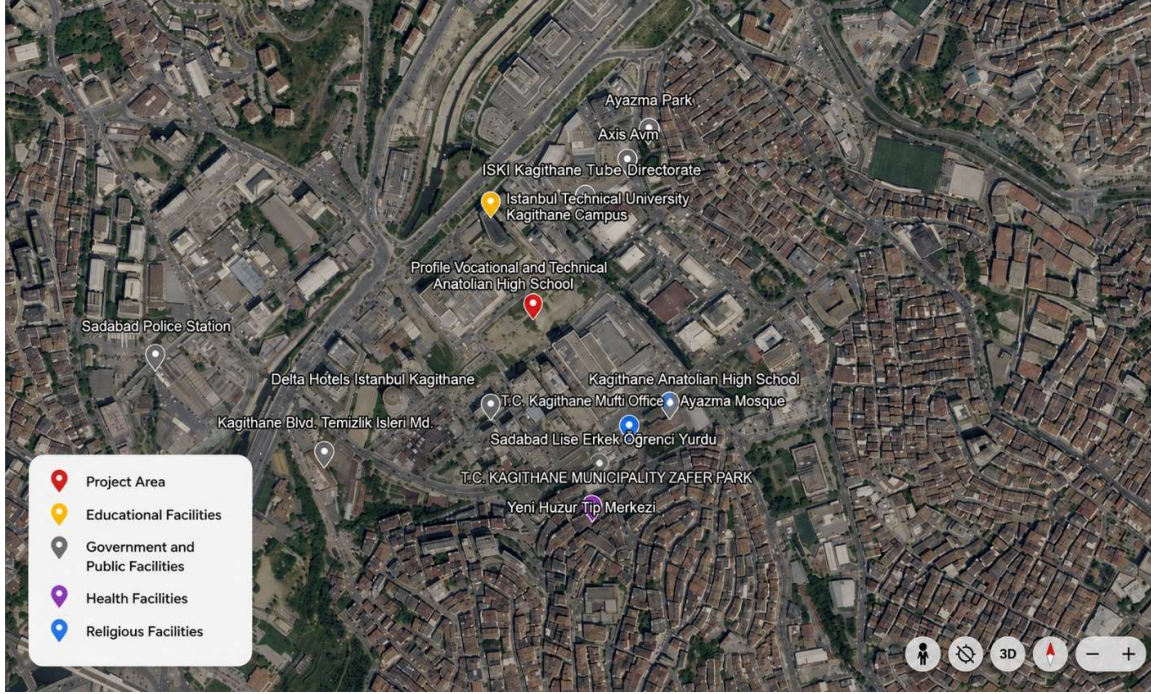


Photo 3: Area of Influence of the project site

ISTANBUL RESILIENCE PROJECT

Annex 3. Land Registration Documents

TAŞINMAZA AİT TAPU KAYDI (Aktif Malikler için Detaylı - ŞBİ var)					
Zemin Tipi	: Ana Taşınmaz	Ada/Parsel	: 7035/3		
Zemin No	: 134502844	Yüzölçüm	: 14.335,02 m2		
İl / İlçe	: İSTANBUL/KAĞITHANE	Ana Taş. Nitelik	: EVVELCE TARLA HALEN FABRIKA VE ARSA		
Kurum Adı	: Kağıthane TM				
Mahalle / Köy Adı	: MERKEZ Mah.				
Mevkii	: CENDERE				
Cilt / Sayfa No	: 477 / 47322				
Kayıt Durum	: Aktif				

TAŞINMAZ ŞERH / BEYAN / İRTİFAK				
S/B/İ	Açıklama	Malik / Lehdar	Tarih - Yevmiye	Terkin Sebebi - Tarih - Yev
Beyan	6306 Sayılı Kanun gereğince riskli yapıdır.		21/11/2013 - 20093	--
Beyan	6306 Sayılı Kanun gereğince riskli yapıdır.		07/11/2016 - 21168	--
Beyan	ORTAK YER : İSTANBUL İLİ KAĞITHANE İLÇESİ MERKEZ Mah. 142 Parsel	MERKEZ Mah. 7035 Ada 3 Parsel	06/11/2024 - 30601	--

MÜLKİYET BİLGİLERİ						
Sistem No	Malik	Elbirliği No	Hisse Pay/Payda	Metrekare	Edinme Sebebi - Tarih - Yev.	Terkin Sebebi - Tarih - Yev.
847098551	KAĞITHANE BELEDİYESİ	190707/716751		381,40	Tevhit İşlemi (TSM) - 06/11/2024 - 30601-	--
847098599	KAĞITHANE BELEDİYESİ	697681/716751		13.953,62	Tevhit İşlemi (TSM) + Birleş. - 06/11/2024 - 30601-	--

* Tesis edilen şerhler ve beyanlar salt elektronik ortamda tutulmaktadır.


Raporlayan: tk38349
Elif YAKAN USTA
Kayıtina Uyandır.
11.12.2024

Rapor Tarihi / Saati : 11.12.2024 10:12

1

ISTANBUL RESILIENCE PROJECT

Annex 4. Topographic Survey

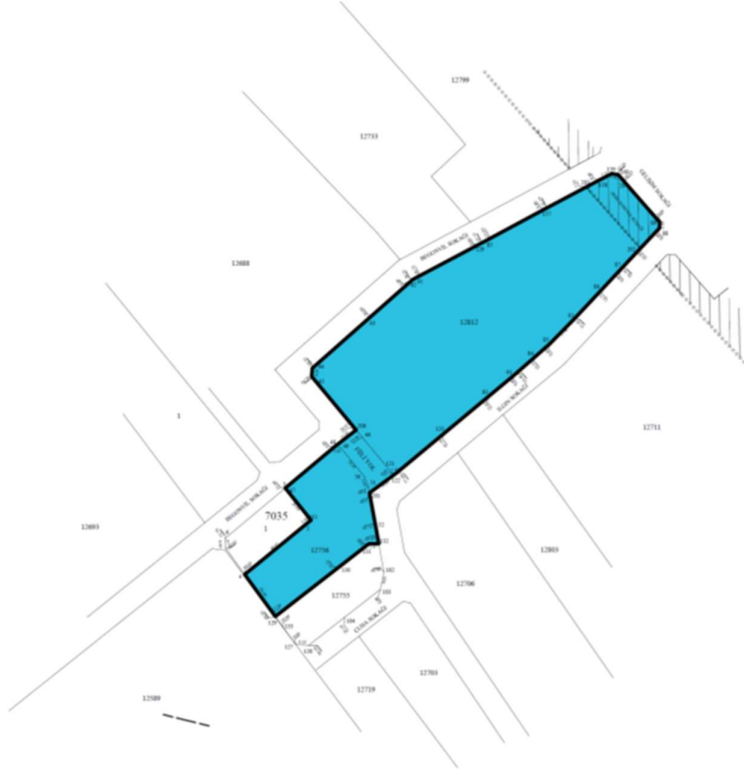

ISTANBUL RESILIENCE PROJECT

Annex 5. Zoning Status Letter

T.C.KAĞITHANE BELEDİYESİ								PLAN VE PROJE MÜDÜRLÜĞÜ	
ADI SOYADI		MAHALLESİ		CADDE-SOKAK		NO.		KAĞITHANE	
KAĞITHANE BELEDİYESİ		MERKEZ		BEGONVİL SOKAĞI					
ALINAN BİLGİLER	EVRAK_KAYIT_NO	RÖPERLİ KROKİ	İMAR DURUMU	TASDIKLI PLAN	PAFTA	ADA	PARSEL		
	GENEL EVRAK								
GÜN	26.11.2024	-	26.11.2024	21.02.2024	F21C20B	7035	3		
SAYI	2813865	-	2813865						



TEKNİK ELEMAN	SERVİS SORUMLUSU	MÜDÜR
AKIF METE Harita Mühendisi	VURAL KAR Harita Mühendisi	MEHMET AVCI Harita Mühendisi

FR.188

İSTANBUL RESILIENCE PROJECT

Annex 6. Official Invitation Letter for the Public Information and Consultation Meeting

T.C.
İSTANBUL VALİLİĞİ
İstanbul Proje Koordinasyon Birimi

Sayı : İPKB/IRP/2026-/...../2026
Konu : Profilo Mesleki ve Teknik Anadolu Lisesi
Çevresel ve Sosyal Yönetim Planı
Paydaş Bilgilendirme ve İstişare Toplantısı

İSTANBUL İL MİLLİ EĞİTİM MÜDÜRLÜĞÜNE

Birimimiz tarafından 2006 yılından bu yana İstanbul Sismik Riskin Azaltılması ve Acil Durum Hazırlık Projesi (İSMEP) yürütülmektedir. Bu süre zarfında İstanbul Proje Koordinasyon Birimi (İPKB), olası bir deprem durumunda kamu yapılarının risklerini azaltmayı hedeflemiş ve Türkiye Hazinesi katkılarıyla projeye dış finansman sağlayarak deprem hazırlık çalışmalarını sürdürmektedir.

Bununla birlikte, günümüzde iklim değişiklikleri ve yaşanan diğer büyük felaketlerden çıkarılan dersler, şehirlerin afet hazırlıklarını daha bütüncül bir yaklaşımla ele alma gerekliliğini ortaya koymuştur. Bu doğrultuda İPKB, Dünya Bankası ile iş birliği içinde "İstanbul Dirençlilik Projesi (IRP)"ni geliştirerek uluslararası standartlara uygun bir risk azaltma ve dirençlilik çerçevesi sunmayı hedeflemektedir.

Bu kapsamda, İstanbul Dirençlilik Projesi'nin "Çevresel ve Sosyal Yönetim Çerçevesi (ÇSYÇ)"nin nasıl uygulanacağına dair bir bilgilendirme ve değerlendirme toplantısı, ilgili kurumların katılımlarıyla, 25 Şubat 2025 tarihinde düzenlenmiştir. Bu süreçte IRP kapsamında yeniden yapımı gerçekleştirilecek olan Profilo Mesleki ve Teknik Anadolu Lisesi için Paydaş Bilgilendirme ve İstişare Toplantısı, 02.07.2026 tarihinde saat 10.00'da Çağlayan Mah. Ayazma Cad. No:22 Kağıthane/İstanbul adresinde bulunan Kağıthane Anadolu Lisesi'nde gerçekleştirilecektir. Profilo Mesleki ve Teknik Anadolu Lisesi taslak sahaya-özel Çevresel ve Sosyal Yönetim Planı www.ipkb.gov.tr web sitemiz üzerinde aşağıdaki bağlantı adresinde tüm taraflarca değerlendirilmek üzere paylaşılmıştır.

<https://www.ipkb.gov.tr/e-kutuphane/cevre-ve-sosyal-dokumanlar/>

Söz konusu toplantıya, Profilo Mesleki ve Teknik Anadolu Lisesi çalışanlarının, öğrenci velilerinin ve ilgili muhtarlık aracılığıyla okul çevresinde yaşayan mahalle sakinlerinin katılım sağlanması büyük önem taşımaktadır. Bu çerçevede, 02.07.2026 tarihinde saat 10.00'da Çağlayan Mah. Ayazma Cad. No:22 Kağıthane/İstanbul adresinde bulunan Kağıthane Anadolu Lisesi'nde gerçekleştirilecek "Paydaş Bilgilendirme ve İstişare Toplantısı"na iştirak edilmesi hususunda gereğini arz ederim.

Yalçın KAYA
Direktör



Kısıklı Mah. Alemdağ Yan Yolu Cad.
No:6 34692 Üsküdar/İSTANBUL

Tel: 0 (216) 505 55 00
Faks: 0 (216) 225 04 85

info@ipkb.gov.tr
www.ipkb.gov.tr

ISTANBUL RESILIENCE PROJECT

Annex 7. Public Announcement of the Consultation Meeting

A. Web Site Announcement



B. Instagram Announcement



ISTANBUL RESILIENCE PROJECT

Annex 8. Minutes of the Public Information and Consultation Meeting

Stakeholder (Group or Individual)	Dates of Consultations	Summary of Feedback	Response of Project Implementation Team	Follow-up Action / Next Steps
Teacher	02.07.2026	It was requested information on the number of school access/circulation arrangements.	The design consultant provided a detailed the architectural design, explaining the main entrance, circulation scheme, and emergency evacuation routes.	-
Teacher	02.07.2026	It was expressed a preference of dense tree planting and extensive post-construction landscaping for their school building area.	The design consultant demonstrated the designated green spaces and tree planting zones on the current landscape plans.	-
Teacher	02.07.2026	It was asked whether adequate indoor and outdoor social spaces would be available for students and staff.	It was demonstrated by design layouts that the spacious entrance halls, expansive foyers, and indoor central atriums are architecturally scaled to function as multi-use social/recreational gathering hubs.	-
Teacher	02.07.2026	It was expressed concerns based on previous experiences about construction quality resulting in roof leaks, window water infiltration, and structural failure of radiator wall mounts; requested rigid construction supervision.	It was outlined the rigorous supervisory and quality control monitoring applied during construction by IPCU site engineers and E&S team. It was clarified that all materials must meet strict technical specifications. Additionally, the standard Defect Liability Period and provisional acceptance framework were detailed as mechanisms to enforce	Monitoring construction activities during the project duration.

ISTANBUL RESILIENCE PROJECT

			contractor accountability.	
		It was emphasized the importance of secure installation of building equipment and fixtures, as well as a reliable electrical and communication cable infrastructure.	It was explained that the building design incorporates a raised-floor system intended to improve the protection and accessibility of electrical and communication infrastructure.	
Teacher	02.07.2026	It was asked whether the IT infrastructure complies with the Ministry of National Education's (MoNE) FATİH Project requirements.	It was explained that the new school design has been prepared to accommodate current MoNE digital infrastructure standards. IPCU further noted that similar systems have been successfully implemented in previous projects without implementation or operational issues.	-
	02.07.2026	It was requested durable, easy-to-maintain and cost-effective building materials. Concerns were also raised regarding the use of concealed reservoirs and sensor-operated faucets due to previous maintenance difficulties and students misuse.	It was explained that material selection is based on the project technical specifications and international procurement requirements.	-
Teacher	02.07.2026	It was asked regarding the physical dimensions and	It was clarified that the perimeter security framework consists of a 1.5-meter reinforced	-

ISTANBUL RESILIENCE PROJECT

		specifications of perimeter boundary fencing to ensure proper student monitoring and campus security.	concrete boundary wall, with additional wire mesh fencing provided above the wall to enhance site security.	
Teacher	02.07.2026	It was asked how the rooftop area would be utilized.	It was explained that the roof is designed to accommodate photovoltaic solar panels to improve energy efficiency.	-

ISTANBUL RESILIENCE PROJECT

Annex 9. Site-Specific ESMP Presentation Materials


Bilgilendirme

Kişisel Verilerin Korunması Kanunu (KVKK) ve Dünya Bankası'nın Bilgi Paylaşımı İlkeleri kapsamında, bu toplantı sırasında ses ve görüntü kaydı alınabileceğini, toplantı katılım listesinde yer alan ad-soyad ve kurum bilgilerinizin toplantının dokümantasyonu ve proje kayıtları amacıyla işleneceğini bildiririz.

Toplantı kapsamında elde edilen bilgiler yalnızca:

- Proje paydaş katılımının kayıt altına alınması,
- Çevresel ve sosyal belge hazırlık süreçlerinin doğrulanması,
- Dünya Bankası'nın şeffaflık ve izleme yükümlülüklerinin karşılanması amaçlarıyla kullanılacak ve üçüncü kişilerle paylaşılmayacaktır.

Toplantıya katılarak bu bilgilendirme kapsamında verilerinizin işlenmesine rıza göstermiş olursunuz.



İSTANBUL VALİLİĞİ İSTANBUL PROJE KOORDİNASYON BİRİMİ

İstanbul Dirençlilik Projesi (IRP)
Profilo Mesleki ve Teknik Anadolu Lisesi Yeniden Yapım
Paydaş Bilgilendirme ve İstisnâ Toplantısı



İSTANBUL PROJE KOORDİNASYON BİRİMİ

Ülke/Bölge : Türkiye / İstanbul
Proje Süresi : 2006 - 2031
Uygulayıcı Kurum : İstanbul Valiliği

İstanbul Proje Koordinasyon Birimi (IPKB)



İstanbul Valiliği altında
Uluslararası kuruluşların kredi / hibelerini kullanan
Projelei paydaş katılımı ile ilgili konularla ilgili içinde yürüten bir birimdir.



Kağıthane İlçesi Eğitim Yatırımlarımız (İSMEP 2006-2026)

KAĞITHANE İLÇESİ KAPSAMINDA YAPILAN ÇALIŞMALAR	
TOPLAM OKUL SAYI:	42
GÜÇLÜNDÜRME VE ONARIM: BAKIMLANAN OKULLAR	35
GÜÇLÜNDÜRME VE ONARIM: DEVAM EDEN OKULLAR	0
YENİDEN YAPIMI BAKIMLANAN OKULLAR	24
YENİDEN YAPIMI DEVAM EDEN OKULLAR	2
YENİDEN YAPIMI İHALE AŞAMASINDAKİ OKULLAR	0
YENİDEN YAPIMI PROJE AŞAMASINDAKİ OKULLAR	1
FİZİBLİTE AŞAMASINDAKİ OKULLAR	0

➢ İSMEP kapsamında Kağıthane İlçesindeki yeniden yapım işlemlerinin toplam sayısı 428 olan eski derslik sayısı 893'e çıkarılmış, toplam kapalı alan da 66.138m²'den 195.403m²'ye yükseltilmiştir.
➢ Yeni İSMEP kapsamında Kağıthane İlçesindeki Güçlendirme ve Onarım işlemlerinin toplam 60.622m² alanı sahip 397 derslikli 28 okul görevi hâle getirmiştir.
➢ Kağıthane İlçesinde 2 adet okulun yeniden yapım inşaat çalışmaları devam etmektedir. 1 okul ise yeniden yapım proje aşamasındadır.



İstanbul Dirençlilik Projesi (IRP)


Dünya Bankası (DB) tarafından finanse edilecek ve İstanbul Valiliği İstanbul Proje Koordinasyon Birimi (IPKB) tarafından yürütülecektir. Proje, İstanbul'un afet risklerini azaltmayı, üstyapıyı güçlendirmeyi ve iklim değişikliğine dayanıklı çözümler geliştirmeyi hedeflemektedir.

PROJE HEDEFİ

- Afetlere dayanıklı ve sürdürülebilir yapısal çözümler geliştirmek,
- İstanbul'un sismik ve iklim risklerine karşı dirençliliğini artırmak,
- Toplumun afetlere hazırlık kapasitesini güçlendirmek,
- Afet risklerini azaltarak sosyal ve ekonomik sürdürülebilirliği desteklemek

ODAK NOKTASI

- İstanbul'un afet ve iklim risklerine karşı dirençliliğini artırmak



Kredi İçeriği

BİLEŞEN 1
Acil Durum Hazırlık ve Müdahale Sisteminin Güçlendirilmesi

BİLEŞEN 2
Kritik Binaların ve Tesislerin Dirençliliğinin Artırılması

İSTANBUL PROJE KOORDİNASYON BİRİMİ



ISTANBUL RESILIENCE PROJECT

Bileşen 1 Kapsamında Yapılması Planlanan Yatırımlar

- Acil Durum Binalarının Dirençli Hale Getirilmesi
- İlk Müdahale Ekiblerinin Eğitimi ve Donatılması
- Toplum Düzeyinde Acil Durum Hazırlığı

IPKB

Bileşen 2 Kapsamında Yapılması Planlanan Yatırımlar

- Kritik Binaların ve Tesislerin Dayanıklılığının Artırılması
- İstanbul'un Uzun Vadeli Afet ve İklim Direncinin Güçlendirilmesi

İSTANBUL PROJE KOORDİNASYON BİRİMİ

IPKB

Proje (IRP) Sonuçları

POO (Proje Geliştirme) Araçları Sonuçları	Ara Sonuçlar	Uzun Vadeli Etki
<ul style="list-style-type: none">İstanbul'un afet ve iklim direncine karşı hazırlık kapasitesinin artırılması,İstanbul'un afet ve iklim direncine karşı müdahale kapasitesinin güçlendirilmesi.	<ul style="list-style-type: none">Acil durumlara müdahale kapasitesinin artırılması,Müdahale ve bilgi sistemlerinin iyileştirilmesi,Mitigasyon ve koruma sistemlerinin güçlendirilmesi,Eğilimler ilk müdahale kapasitesinin artırılması,Kritik binaların afete dayanıklı ve önemdeki temel hizmetleri sağlamaya devam etmesi,Kararlı durumda sosyal dayanıklılığın ve afetlere karşı dayanıklılığın artırılması,Dirençli afetlere ve kentsel dönüşüm için harekete geçirilmesi iyileştirilmesi,Özellikle afetlere dayanıklı yapılar ve hizmetlerin artırılması,Afet ve iklim direnci konusunda kentsel kapasitenin artırılması,	<ul style="list-style-type: none">İstanbul'un afet ve iklim direncinin artırılması,İstanbul'un afet ve iklim direncine karşı hazırlık ve müdahale kapasitesinin artırılması,Acil durumlara müdahale kapasitesinin ve kentsel dayanıklılığın artırılması olarak dirençli hale getirilmesi.

IPKB

Çevresel ve Sosyal Yönetim Gerekliliği

Projenin ana faaliyeti olan inşaat çalışmaları sırasında;

- Proje alanında ve çevresinde ortaya çıkabilecek olası çevresel ve sosyal etkilerin en aza indirilmesi,
- Ulusal mevzuat ve Dünya Bankası Çevresel ve Sosyal Standartlarına (ÇSS) uyumun sağlanması,
- İşgücü haklarının korunması,
- Toplum sağlığı ve güvenliğinin gözetilmesi,
- Çevresel ve sosyal risklerin etkin ve sistematik şekilde yönetilmesi amacıyla çevresel ve sosyal yönetim süreçlerinin uygulanması gerekmektedir.

Bu kapsamda;

- Ulusal ve uluslararası standartlara uygun önleyici ve azaltıcı tedbirler uygulanacak,
- Olası olumsuz etkiler önlenerek, önlenemeyen durumlarda kabul edilebilir seviyelere indirilecektir,
- Çevresel ve sosyal performans, uygulama süreci boyunca izlenecek ve raporlanacaktır.

IPKB

Dünya Bankası Çevre ve Sosyal Standartları (ÇSS)

- Çevresel ve Sosyal Risklerin ve Etkilerin Değerlendirilmesi ve Yönetilmesi
- İşgücü ve Çalışma Koşulları
- Kaynak Verimliliği, Kirliliğin Önlenmesi ve Yönetimi
- Toplum Sağlığı ve Güvenliği
- Arazi Edinimi, Arazi Kullanımına İlgili Kısıtlamalar ve Gönlülsüz Yeniden Yerleşim
- Biyolojik Çeşitliliğin Korunması ve Yaşayan Doğal Varlıkların Sürdürülebilir Yönetimi
- Yetersiz Hizmet Alan Geleneksel Yerel Topluluklar (Yerli Halklar, Sahra Altı Afrika)
- Kültürel Miras
- Finansal Araçlar
- Paydaş Katılımı ve İstişare

IPKB

Dünya Bankası Çevresel ve Sosyal Standartları (ÇSS)

- ÇSS1 Çevresel ve Sosyal Risklerin ve Etkilerin Değerlendirilmesi ve Yönetilmesi
- ÇSS2 İşgücü ve Çalışma Koşulları
- ÇSS3 Kaynak Verimliliği, Kirliliğin Önlenmesi ve Yönetimi
- ÇSS4 Toplum Sağlığı ve Güvenliği
- ÇSS10 Paydaş Katılımı ve İstişare

IPKB

ISTANBUL RESILIENCE PROJECT

Dünya Bankası Çevresel ve Sosyal Standartları

Banka, çevresel ve sosyal prosedürlerin bir parçası olarak tüm projeleri dört sınıflandırmadan birine tabii tutmaktadır: **Yüksek Risk, Önemli Risk, Orta Risk ve Düşük Risk.**

Uygun risk sınıflandırmasını belirlerken Banka şu konuları dikkate alır:

- Projenin türü, yeri, hassasiyeti ve ölçeği;
- Potansiyel çevresel ve sosyal risklerin ve etkilerinin niteliği ve büyüklüğü;
- Kredi kullanıcısının çevre ve sosyal riskleri ve etkileri Çevre ve Sosyal Standartlarına tutarlı bir şekilde yönetme kapasitesi ve taahhüdü.

IPKB

Yayınlanan IRP Ç&S Dokümanları

Paydaş Katılım ve Bütçeleme Toplantılarında Nihai versiyonları oluşturulmuş ve Onaylanmış Çevre ve Sosyal dokümanlar Türkçe ve İngilizce olarak www.ipkb.gov.tr sitemizde 03.05.2025 tarihinde tüm ilgili tarafların erişimibilmesi için paylaşılmıştır.

- ÇSTP → Çevre ve Sosyal Taahhüt Planı
- ÇSYÇ → Çevre ve Sosyal Yönetim Çerçevesi
- İRP → İşletici Yönetim Prosedürleri
- PKP → Paydaş Katılım Planı

IPKB

Yeniden Yapım Projesi Hakkında

Profilo Mesleki ve Teknik Anadolu Lisesi yeniden yapım projesi:

Bilgen 2. Kitap Binaların ve Bahçelerin Dayanıklılığının Artırılması kapsamında finanse edilecek ilk projelerden biri olarak seçilmiştir.

Proje Hedefi

- Okulu en yüksek sismik ve iklim dirençli standartlarına göre yeniden inşa etmek
- Aktifler sayısı **72** saat temel hizmetleri (elektrik, su, yitirizk ve ısıtma) sağlayabilen kendi kendine yeten bir bina inşa etmek
- Azul inşaatlılık kapasitesinin artırılması ve eğitim alanlarının sağlanmasına katkıda bulunmak

IPKB

İPKB Görev ve Sorumlulukları

- Gözetim Proje Yürütme ve Uygulama
- Paydaş Katılım ve Bilgilendirme
- Çevresel ve Sosyal İzleme
- Teknik ve Finansal Danışmanlık Hizmetleri
- İşletim ve Bakım Hizmetleri
- İzlem ve Değerlendirme

IPKB

İlgili Kamu Kurum ve Kuruluşlarının Proje Kapsamındaki Genel Sorumlulukları

İPKB ile yakın koordinasyon içinde çalışarak planlamaları eksiksiz yürütmesini sağlamak,

İnşaat prosedürleri diğer sınıflandırmaları göz önünde tutularak, yer belediyesi zamanında yapmak, proje sonunda kabul edilmiş ve ilgili standartlara uygun olarak,

Proje uygulanmasına yönelik gerekli belge ve dokümanları zamanında (Bakım Servisi, Gözetim Hizmetleri, Maliyet Maliyet ve İhtisapları sağlamak),

Paydaşların gelen geri bildirimlerini ve şikayetlerini İPKB'ye iletilmesini sağlamak,

Aktif soruları sorularını zamanında yanıtlanmasını sağlamak,

Konu binalarının ve diğer yapıların aktif soruları binalarına hata hata giderilmesi,

Sıkımların periyodik bakım ve onarımlarının yapılmasını sağlamak ve diğer çalışmalarını sağlamak.

IPKB

PROFİLO MESLEKİ VE TEKNİK ANADOLU LİSESİ YENİDEN YAPIM İŞİ

İPKB Ç&S YÖNETİM SORUMLULUKLARIMIZ

- Proje'nin tüm yaşam döngüsü boyunca, projeye ilişkin tüm görsel materyaller, broşürler, Şikayet Mekanizması (SM) bilgileri ve dokümantasyon (Çevresel ve Sosyal dokümanlar dâhil olmak üzere) tüm paydaşların erişimine açık olacak şekilde İPKB web sayfası üzerinden kamuoyuyla paylaşılacaktır.
- Bu taahhüt, Paydaş Katılım Planı (PKP) ve projeye ilişkin diğer dokümanlarda tanımlanan proje standartlarına tam uyum içinde yerine getirilecektir.
- İstanbul Proje Koordinasyon Birimi'nin (İPKB) temel sorumluluğu, söz konusu proje standartlarına tam uygunluk sağlayacak şekilde, bu şeffaf ve tutarlı bilgi paylaşım sürecini aktif olarak temin etmek ve sürdürmektir.

IPKB

ISTANBUL RESILIENCE PROJECT


DB Ç&S Risk Değerlendirmesi

Dünya Bankası saha tarama sonucuna göre Profilo Mesleki ve Teknik Anadolu Lisesi Yeniden Yapım Projesi;

- Çevresel Riski **Orta**,
- Sosyal Riski **Orta**,

olarak belirlenmiştir.

IPKB

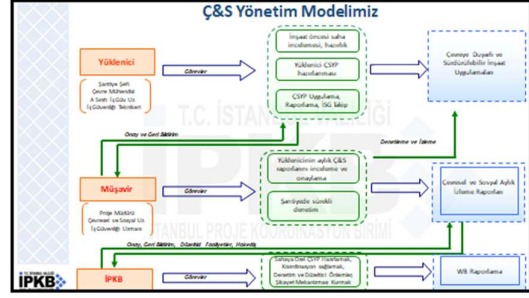

ÇEVRESEL RİSKLERİN YÖNETİMİ

İnşaat çalışmaları sırasında, bölgede halihazırda mevcut olan ulayım güzergahları, kanalizasyon, elektrik ve su şebekeleri kullanılacaktır.

ATIK YÖNETİMİ

İnşaat ve Hafriyat	Evvel Atıklar	Tehlikeli Atıklar
<ul style="list-style-type: none"> Belediye'nin belirlediği alanlara taşınarak depolanır. Resmî yazılar ile hafriyat izin ve taşıma belgeleri alınır. 	<ul style="list-style-type: none"> Kaymağında saygınlıklar (plastik, cam, kâğıt vb.). Geri dönüşüme katılm sağlanır. Yoksa; Belediye bünyesine teslim edilir. 	<ul style="list-style-type: none"> Tehlikeli ve kimyasal atıklar için saha kapsamında "Atık Geçici Depolama Alanı" oluşturulur. Çevre Şehircilik ve İklim Değişikliği Bakanlığı UÇBŞ tarafından hazırlanmış standart teorisine göre yapılır.

Atıkların taşınması ve depolanması sırasında, çevre ve insan sağlığı açısından gerekli tedbirler alınacaktır.

IPKB

ÇEVRESEL RİSKLERİN YÖNETİMİ

Top Kontrolü:

- İnşaat faaliyetleri sırasında oluşabilecek toz emisyonları, özellikle kuru hava koşullarında sulama yapılarak kontrol altına alınacaktır.
- Malzeme nakliyesi sırasında kamyon kasaları **branda** ile kapatılacak; hafriyat veya dolgu malzemelerinin rüzgarla çevreye yayılması engellenecektir.
- Toz oluşturabilecek malzemeler (num, çakıl, çimento vb.) **kapalı alanlarda depolanacak veya üstü uygun şekilde örtülecektir.**
- Çalışma mekanizması kapsamında tozla ilgili gelen geri bildirimler hızla değerlendirilerek ek tedbirler uygulanacaktır.

Günlük Kontrolü:

- Çalışmalar mümkün olduğunca **gündüz** saatlerinde yürütülecektir.
- Ses oluşturan ekipmanların **günyüzde** bakımını yapılarak **gürültü** seviyeleri minimumda tutulacaktır.
- Yüksek gürültülü işler kapsamında yakın mahalleler veya kullanıcılar bilgilendirilecek, **çalışma programı önceden duyurulacaktır.**
- En yakın alıcılardan **gürültü** üretilmeye ilişkin herhangi bir şikayet alındığında **gürültü ölçümleri** yapılacaktır.

IPKB

Çevre ve Atık Yönetimi

1 İnşaat esnasında başlıca dikkat edilecek hususlar

- ✓ Top kontrolü
- ✓ Gürültü kontrolü
- ✓ Toprak kirliliği
- ✓ Toz ve yavaş göçme
- ✓ Ağaçların korunması

IPKB

Çevre ve Atık Yönetimi

2 Atıkların türüne göre ayrı toplama depolanması

- ✓ Tehlikeli atıklar
- ✓ Tehlikeli olmayan (jevvel ve geri dönüştürülebilir atıklar)
- ✓ Atık orosno göre ayrı konteynörler

3 Sahada "Atık Yönetimi Yönetmeliğine" uygun "Atık Geçici Depolama Alanı" kurulması

- ✓ Üstü kapalı, kilitli, ayrı bölmeler
- ✓ Güvenli sığınak
- ✓ Atık alanı sınırlanmış ve işaretli
- ✓ İşletim izni
- ✓ Güven izni
- ✓ Yangın söndürücü

IPKB

ISTANBUL RESILIENCE PROJECT

Çevre ve Atık Yönetimi

4 Lisanslı taşıyıcı firmalar ile gönderim ve Atık kayıtlarının tutulması

- ✓ ÇKSİ lisanslı taşıyıcılar ile taşıma ve teslim
- ✓ Atık taşıma belgesi ile atıkların taşıma işlemi gönderimden önce onaylanmalıdır.

IPKB

SOSYAL RİSKLERİN YÖNETİMİ

- Çalışmalar, çevrede yaşayanların günlük hayatını en az etkileyecek şekilde yürütülecek, çalışma saatleri buna göre planlanacaktır.
- Araç giriş-çıkışları için trafik yönetim planı uygulanacak, malzeme taşıyan araçların hız ve güzergâhları denetlenecektir.
- Şantiyedeki tüm çalışanlara davranış kuralları (ayrımçılık, SEA/SH vb.) konusunda eğitim verilecek ve bu kurallara uyum sağlanacaktır.
- Halkla düzenli iletişim için Şikâyet Mekanizması işi iletilecek, başvurular kayıt altına alınıp hızlı şekilde çözülecektir.
- Proje istihdamının artmasıyla bölgedeki esnafın ekonomik olarak olumlu etkilenmesi beklenmektedir.
- İnşaat alanında güvenlik, uyarı levhaları ve bariyerler sağlanarak yetkiz kişilerin girişinin önüne geçilecek ve mahalle güvenliği korunacaktır.

IPKB

PROJEYE ÖZEL ÇEVRESEL VE SOSYAL YÖNETİM PLANI

IPKB

İSTANBUL BİRENCİLİK PROJESİ

PROJE ÖZEL ÇEVRESEL VE SOSYAL YÖNETİM PLANI

ÇEVRESEL VE SOSYAL YÖNETİM PLANI

İSTANBUL BİRENCİLİK PROJESİ

ORDİNASYON BİRİMİ

https://www.ipkb.gov.tr/fon-istemleri/fonbaski/2026/06/CSYP_kitapca_Profilo.pdf

IPKB

YÜKLENİCİ ÇŞYP VE EK PLANLARI

- Atık Yönetim Planı
- Toplum Sağlığı ve Güvenliği Planı
- Trafik Yönetimi Planı
- İş Sağlığı ve Güvenliği (İSG) Planı
- Yüklenicinin İş Gücü Yönetim Planı (Proje İYB ile uyumlu olarak)
- Proje Düzeyinde Paydaş Katılım Planı (Project PKP ile uyumlu olarak)
- Yüklenici Şikâyet Mekanizması (ŞM) Prosedürleri (İşçiler ve topluluklar için)
- Şans Eseri Buluntu Prosedürleri

IPKB

Şikâyet Mekanizması ve Kanalları

Projenin sosyal ve çevresel etkilerinden doğrudan ya da dolaylı olarak etkilenen paydaşların endişe/sorum/görüş/şikâyetleri kayıt altına alınarak, 15 iş gününde çözüme kavuşturulacaktır.

ŞİKAYET FORMU/E-POSTA

<https://www.ipkb.gov.tr/sikayet/formu/>

info@ipkb.gov.tr

Twitter: <https://www.com/sikbayit/>

Facebook: <https://www.facebook.com/sikbayit/>

Instagram: <https://www.instagram.com/sikbayit/>

LinkedIn: @IPKB

IPKB

Şikâyet Mekanizması Kanalları

İSTANBUL VALİLİĞİ VE BB

Açık Kapı : Bankalar vasıtasıyla yüz yüze

Beyaz Masa : 153 Çağrı Merkezi, <https://www.istanbul.gov.tr/>

İSTANBUL VALİLİĞİ

CİMER

Portal : <https://www.cimer.gov.tr/>

Çağrı Merkezi : 150

YİMER

Web Sitesi : <http://www.yimer.gov.tr/>

Çağrı Merkezi : 157

IPKB



GELECEĞİMİZİ GÜÇLENDİRİYORUZ...

İSTANBUL VALİLİĞİ

İSTANBUL PROJE KOORDİNASYON BİRİMİ

IPKB

İstanbul Proje Koordinasyon Birimi

www.ipkb.gov.tr/ [Facebook](https://www.facebook.com/ipkb.gov.tr/) [Instagram](https://www.instagram.com/ipkb.gov.tr/) [LinkedIn](https://www.linkedin.com/company/ipkb.gov.tr/)

IPKB

ISTANBUL RESILIENCE PROJECT

Annex 10. Project Design Presentation

IPKB

PROFİLO MESLEK VE TEKNİK ANADOLU LİSESİ



optimal

IPKB

GÖRSELLER



optimal

IPKB

GÖRSELLER



optimal

IPKB

optimal

GÖRSELLER



optimal

IPKB

optimal

GÖRSELLER



optimal

IPKB

optimal

GÖRSELLER



optimal

IPKB

optimal

Yerleşim Planı

Kullanılabilir Kapalı İnşaat Alanı

A BLOK: 3.963,70 m² / 18x20+0NKK
B BLOK: 14.524,70 m² / 18x20+0NKK
C BLOK: 2.437,30 m² / 18x20+0NKK
D BLOK: 3.630,00 m² / 18x20+0NKK
E BLOK: 1.899,48 m² / 18x20

Toplam İnşaat Alanı: 25.512,80 m²

Parsel Bilgisi: 7035 / 3
Arsa Alanı: 14.335,02 m²



optimal

IPKB

optimal

Vaziyet Planı

Yeni Tepebağ Çukurlu Vaziyet Planı

C BLOK
BİLİGİM
TEKNOLOJİLERİ AT.

E BLOK
SOSYAL TİSİS

D BLOK
ELEKTRİK &
ELEKTRONİK AT.

R BLOK
OKUL

A BLOK
ÖĞRETİM EVİ

Yaya Geçiş Çıkışı

Araç Geçiş Çıkışı

Beyoğlu Çk

İşgali Çk



optimal

IPKB

optimal

ISTANBUL RESILIENCE PROJECT

B BLOK / 1. Kat Planı

İstat. Hacimler Alan: 103,4 m² Teknik & Sigortak Alanları Alan: 8,2 m² İstat. Birim Alan: 124,8 m² Depo Alan: 63,4 m² Aktif Laboratuvar Alan: 69,4 m²



B BLOK / 2. Kat Planı

İstat. Hacimler Alan: 103,7 m² Teknik & Sigortak Alanları Alan: 8,2 m² İstat. Birim Alan: 125,3 m² Depo Alan: 63,4 m² Aktif Laboratuvar Alan: 69,4 m²



B BLOK / 3. Kat Planı

İstat. Hacimler Alan: 103,4 m² Teknik & Sigortak Alanları Alan: 8,2 m² İstat. Birim Alan: 124,8 m² Depo Alan: 63,4 m² Aktif Laboratuvar Alan: 69,4 m²



B BLOK / 4. Kat Planı

İstat. Hacimler Alan: 97,4 m² Teknik & Sigortak Alanları Alan: 12 m² İstat. Birim Alan: 109,2 m² Depo Alan: 47,2 m² Aktif Laboratuvar Alan: 124,3 m²



C BLOK / Bodrum Kat Planı

TEKNİK ALAN & DEPO
Alan: 174,29 m²




C BLOK / Zemin Kat Planı

ATÖLYE Alan: 102,44 m² İDARE ALANI Alan: 72,07 m² İSLAK HACİM Alan: 37,21 m² TEKNİK ALAN & DEPO Alan: 23,15 m²




C BLOK / 1. Kat Planı

LABORATUVAR Alan: 273,54 m² İDARE ALANI Alan: 15,03 m² İSLAK HACİM Alan: 37,21 m² TEKNİK ALAN & DEPO Alan: 12,58 m²



C BLOK / 2. Kat Planı

LABORATUVAR Alan: 108,36 m² İDARE ALANI Alan: 15,00 m² İSLAK HACİM Alan: 37,21 m² ATÖLYE Alan: 101,16 m² TEKNİK ALAN & DEPO Alan: 12,58 m²



ISTANBUL RESILIENCE PROJECT

Annex 11. Consultation Meeting Photographs

